

PHOTOGRAPHS

PHOTOGRAPH #1



BUILDING 26 SECTION C

Kick out flashing detail complete. Roof tiles have not been re-installed.

PHOTOGRAPH #2



BUILDING 26 SECTION G

Owner's representative walked building with Contractor and Delta. Several punch items were marked and noted. The punch list will be provided by Delta.

PHOTOGRAPH #3



**BUILDING 26
SECTION B**

Owner's representative walked building with Contractor and Delta. Several punch items were marked and noted. The punch list will be provided by Delta.

PHOTOGRAPH #4



**BUILDING 26
SECTION D- UNIT #2627**

Window identified as inoperable during interior punch walkthrough has been repaired.

PHOTOGRAPH #5



**BUILDING 27
SECTION G**

Contractor has primed and painted new stucco.

PHOTOGRAPH #6



**BUILDING 27
SECTION F**

Stucco sub – contractor has applied sand and finish texture coats at portions of the section.

PHOTOGRAPH #7



**BUILDING 27
SECTION F**

Stucco accessories and lath have been completed and inspected for compliance.

PHOTOGRAPH #8



**BUILDING 27
SECTION E**

Stucco weep accessory being installed at base of wall.


PHOTOGRAPH #9



**BUILDING 27
SECTION E**

Unit #2718- Contractor has applied interior sealant bead to window and in process of repairing drywall.

PHOTOGRAPH #10

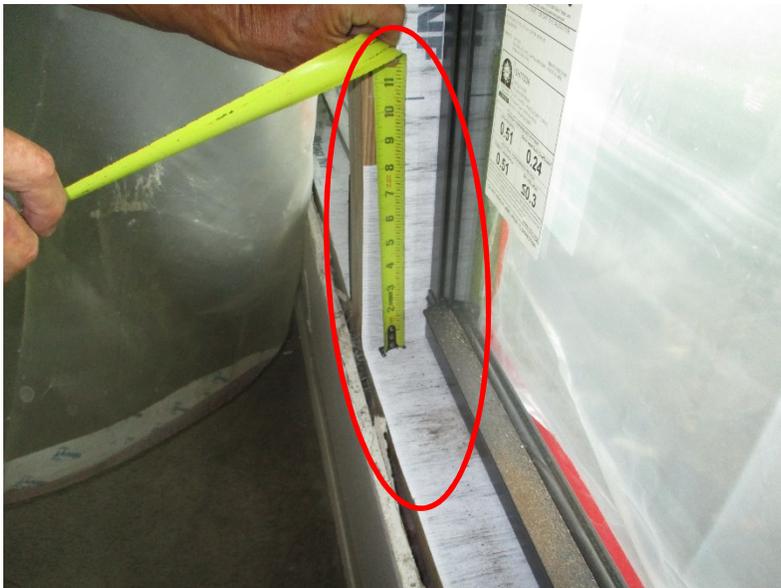

**BUILDING 27
SECTION E**

Unit #2718- DuPont flashing inspected for proper installation and overlapping.


PHOTOGRAPH #11



**BUILDING 27
SECTION E**

Unit #2718- Window installation checked for proper fit and dimensions.

PHOTOGRAPH #12

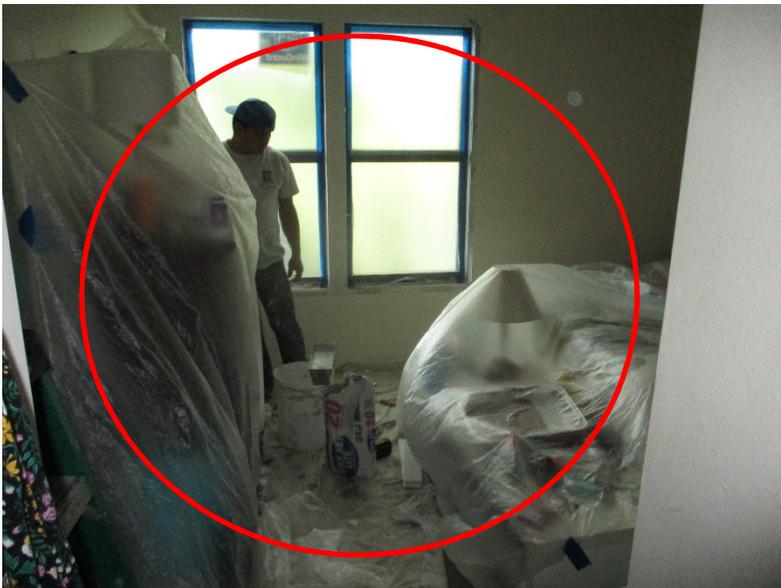

**BUILDING 27
SECTION E**

Unit #2718- Contractor is covering owner's property to avoid damage while repairs are in progress.


PHOTOGRAPH #13



**BUILDING 27
SECTION C**

Tyvek WRB and new windows have been installed and inspected for compliance.

PHOTOGRAPH #14

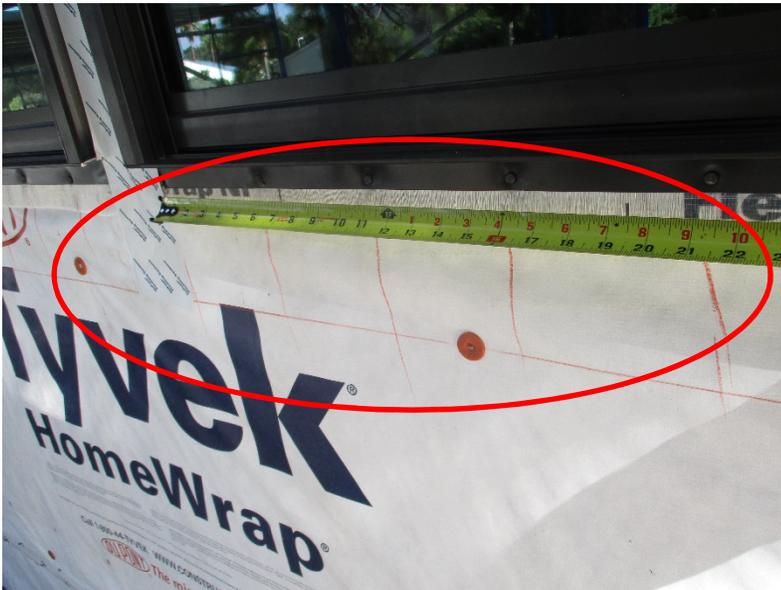

**BUILDING 27
SECTION C**

Tyvek WRB and new windows have been installed and inspected for compliance.

PHOTOGRAPH #15



**BUILDING 27
SECTION C**

Tyvek WRB and new windows have been installed and inspected for compliance.

PHOTOGRAPH #16



**BUILDING 27
SECTION C**

Contractor has installed kick out flashing at new sheathing to deck transitions.

PHOTOGRAPH #17



**BUILDING 27
SECTION B**

Contractor has repaired damaged framing and installed Simpson Strong-Tie connectors.


PHOTOGRAPH #18



**BUILDING 27
SECTION B**

Roof sheathing is damaged by previous roofing leaks and is to be repaired by owner's contractor.

PHOTOGRAPH #19

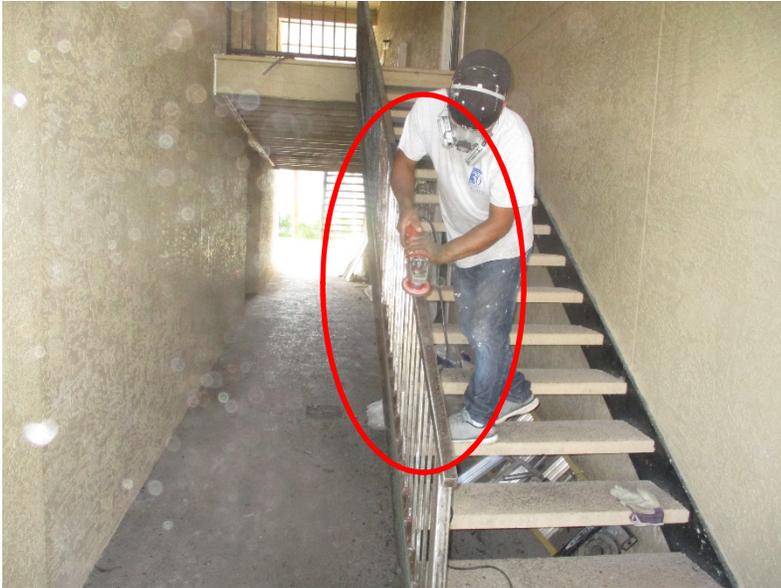

**BUILDING 27
SECTION A**

Contractor has begun to prepare metal railings for primer at stairways.
