

PHOTOGRAPHS

PHOTOGRAPH #1



BUILDING 24 BALCONY RAILING

Contractor is priming railing with #931 Encapsulon Industrial Epoxy Mastic primer.

PHOTOGRAPH #2



BUILDING 24 BALCONY RAILING

Contractor has finished balcony railing with Scot-Thane Acrylic gloss enamel.


PHOTOGRAPH #3



**BUILDING 24
SECTION C**

Contractor has begun installing painted railings.

PHOTOGRAPH #4

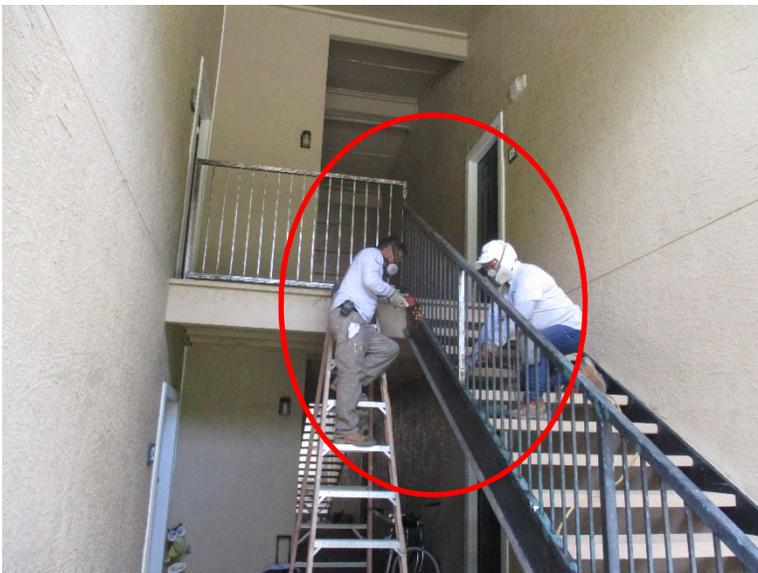

**BUILDING 24
SECTION E**

Contractor is preparing breezeway railings by removing peeling paint and rust.


PHOTOGRAPH #5



**BUILDING 24
SECTION G**

Contractor is preparing breezeway railings by removing peeling paint and rust.

PHOTOGRAPH #6

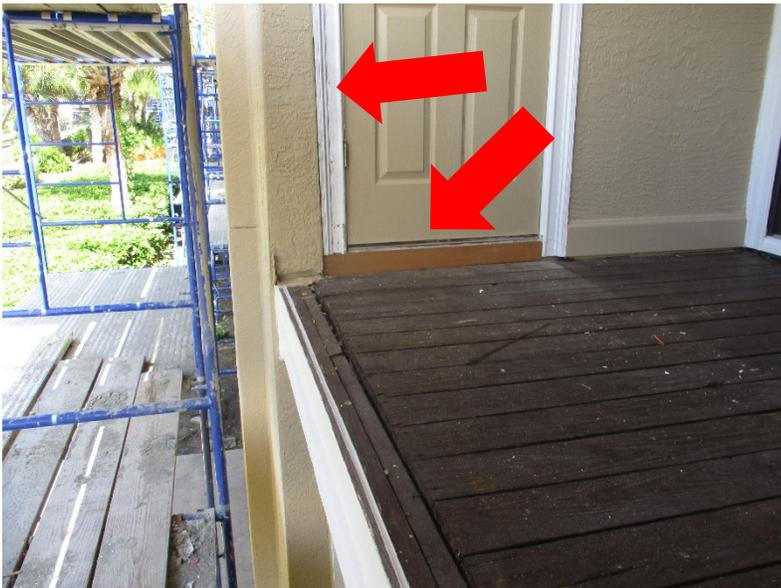

**BUILDING 24
SECTION G -UNIT #2422**

Door trim and door sill have been replaced.

PHOTOGRAPH #7



**BUILDING 24
SECTION F -UNIT #2416**

Interior flashings and sealants installed at window sills as required. Drywall repairs in progress.

PHOTOGRAPH #8



**BUILDING 24
SECTION F**

Contractor has applied primer and finish paint at stucco walls and balcony wood trim.

PHOTOGRAPH #9



**BUILDING 24
SECTION E**

Contractor has applied primer and finish paint at stucco walls and balcony wood trim.


PHOTOGRAPH #10



**BUILDING 26
SECTION H**

Sub-Contractor has applied scratch coat of stucco and begun application of brown coat.


PHOTOGRAPH #11

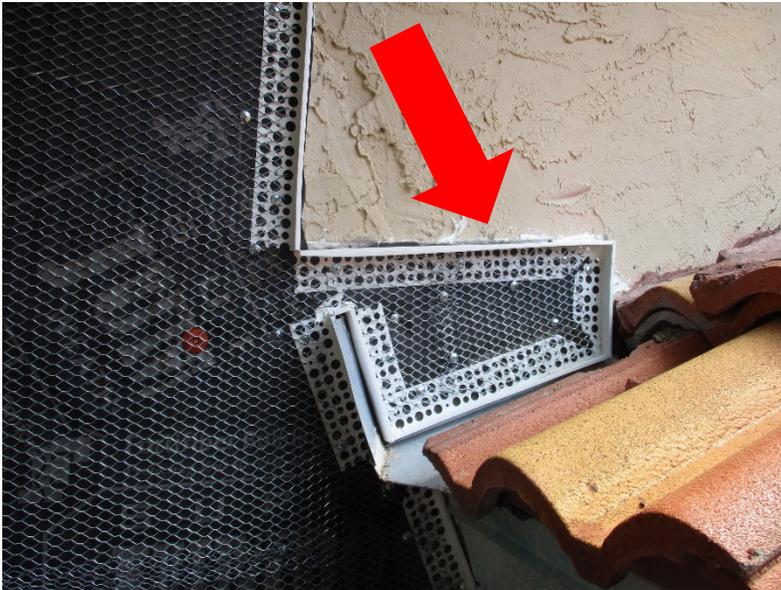

**BUILDING 26
SECTION B**

Contractor has made corrections at kick out flashing and stucco sub-contractor has applied accessories and lath in preparation for stucco.

PHOTOGRAPH #12

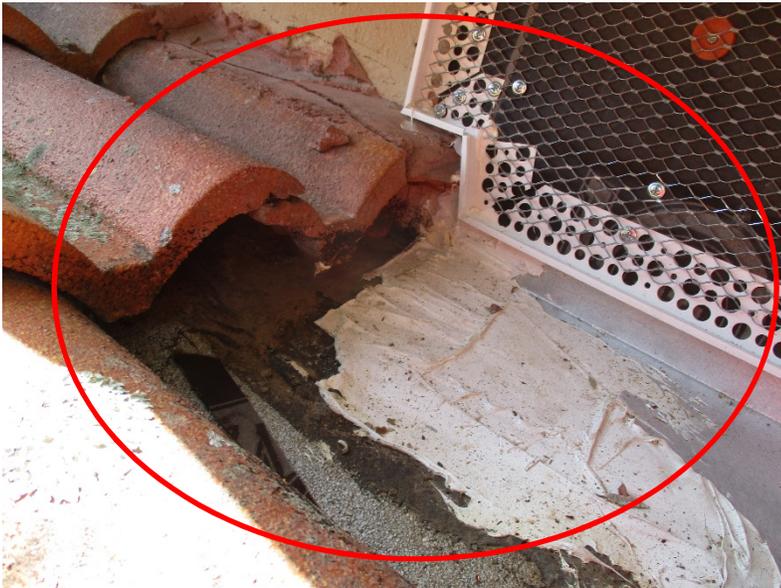

**BUILDING 26
SECTION C**

Kick out roof flashing has been installed incorrectly over roofing materials.

PHOTOGRAPH #13



**BUILDING 26
SECTION B**

Stucco Sub-contractor is installing stucco accessories and lathing in preparation for stucco.

PHOTOGRAPH #14



**BUILDING 26
SECTION C**

Tyvek WRB has been applied over new sheathing in preparation for window installations.

PHOTOGRAPH #15



**BUILDING 26
SECTION D**

Plywood sheathing inspection marked for corrections.

PHOTOGRAPH #16



**BUILDING 26
SECTION E**

Breezeway columns and built up beams do not show damage to framing and will not require framing repairs.

PHOTOGRAPH #17



**BUILDING 26
ATTIC #2628**

Contractor has completed scab and gusset repairs at damaged truss framing.

PHOTOGRAPH #18



**BUILDING 26
SECTION E**

Damages have been identified and marked for repairs.

PHOTOGRAPH #19



**BUILDING 26
SECTION E**

Damages have been identified and marked for repairs.

PHOTOGRAPH #20



**BUILDING 26
SECTION D**

Contractor has made sheathing corrections, installed Tyvek HomeWrap WRB and is installing PPG windows.

PHOTOGRAPH #21



**BUILDING 26
SECTION F**

Contractor has erected scaffolding and begun demo work at walls and balconies.

PHOTOGRAPH #22



**BUILDING 26
SECTION F**

Damage to wood framing at window identified and marked for repairs.
