

PHOTOGRAPHS

PHOTOGRAPH #1



BUILDING 24 BALCONY RAILING

Contractor is priming railing with #931 Encapsulon Industrial Epoxy Mastic primer.

PHOTOGRAPH #2



BUILDING 24 BALCONY RAILING

Contractor has finished balcony railing with Scot-Thane Acrylic gloss enamel.


PHOTOGRAPH #3



**BUILDING 24
SECTION B**

Repairs being made at kick out flashings where stucco was notched out incorrectly.

PHOTOGRAPH #4

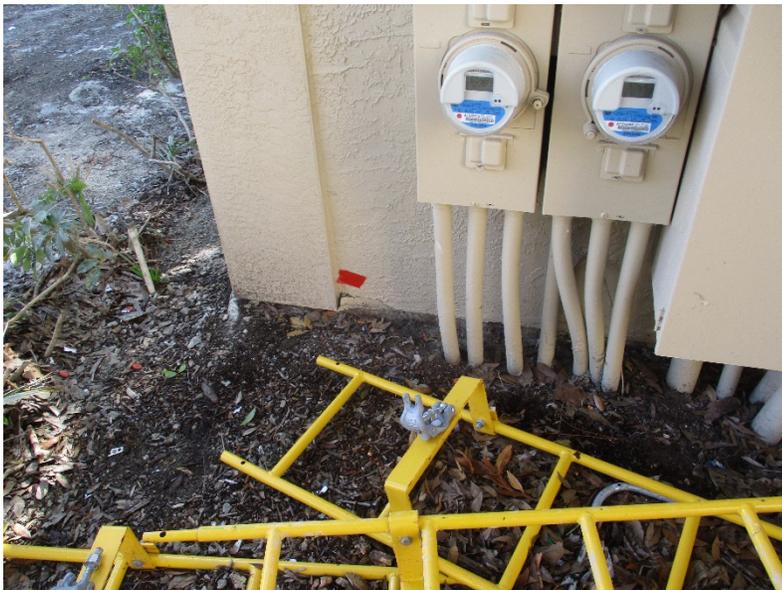

**BUILDING 24
SECTION D**

Pre-punch by Delta identified stucco repair to be made.


PHOTOGRAPH #5



**BUILDING 24
SECTION D**

Stucco repaired, previously identified and marked by Delta pre-punch.

PHOTOGRAPH #6

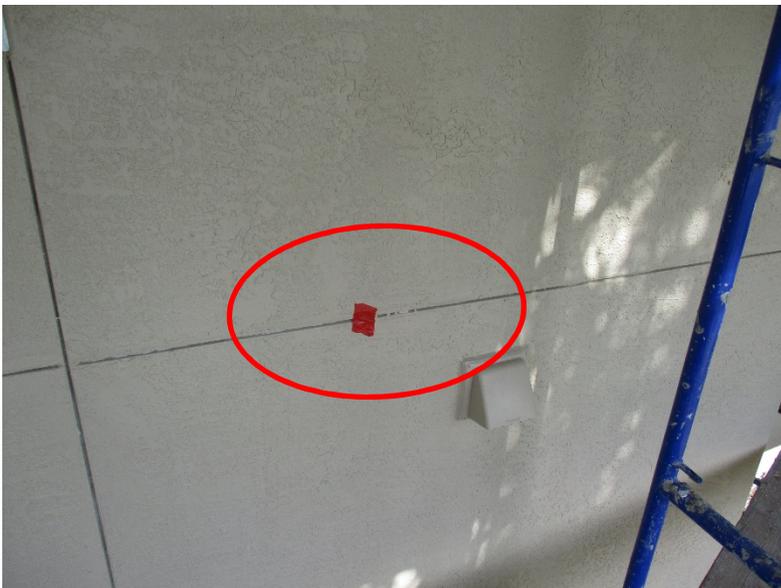

**BUILDING 24
SECTION H**

Other details marked by Delta pre-punch. Stucco or paint has bridged control joint and will be removed and touched up.

PHOTOGRAPH #7



**BUILDING 24
SECTION H**

Paint on dryer vent covers is distorted and will require re-painting.

PHOTOGRAPH #8



**BUILDING 24
SECTION C**

Contactor has removed scaffold and materials and has begun site cleanup of grounds around building.

PHOTOGRAPH #9



**BUILDING 26
SECTION H**

Sub-Contractor has applied finish coat of stucco and in process of moisture curing.

PHOTOGRAPH #10



**BUILDING 26
SECTION A**

Stucco sub-contractor is applying brown coat over scratch coat at breezeway area.

PHOTOGRAPH #11



**BUILDING 26
SECTION B**

JumboTex WRB, stucco accessories and lath have been applied in preparation for stucco.

PHOTOGRAPH #12



**BUILDING 26
SECTION B**

Stucco Sub-contractor is applying new stucco in three coat system.

PHOTOGRAPH #13



**BUILDING 26
SECTION C**

JumboTex WRB, stucco accessories and lath are being applied in preparation for stucco.


PHOTOGRAPH #14



**BUILDING 26
SECTION D**

Stucco sub-contractor has begun to install JumboTex WBR.

PHOTOGRAPH #15

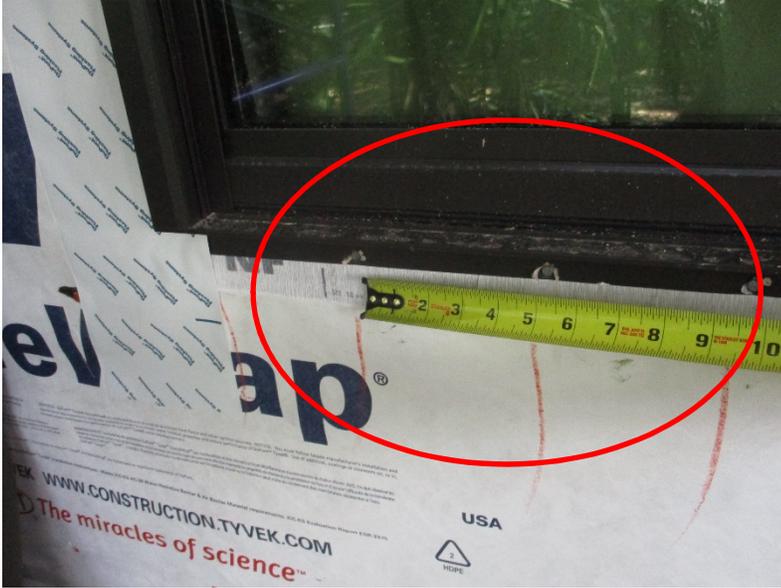

**BUILDING 26
SECTION D**

Window flanges have been fastened in accordance with manufactures NOAs.

PHOTOGRAPH #16



**BUILDING 26
SECTION E**

Roof sheathing damaged. Repairs are to be done by roofing contractors for owners.

PHOTOGRAPH #17



**BUILDING 26
SECTION F**

Roof sheathing damaged. Repairs are to be done by roofing contractors for owners.

PHOTOGRAPH #18



**BUILDING 26
SECTION F**

Damages at balcony built up beams, columns and wall framing have been identified and marked for repairs.

PHOTOGRAPH #19



**BUILDING 26
SECTION F**

Damages at balcony built up beams, columns and wall framing have been identified and marked for repairs.

PHOTOGRAPH #20



**BUILDING 26
SECTION F**

Damages at balcony built up beams, columns and wall framing have been identified and marked for repairs.

PHOTOGRAPH #21



**BUILDING 26
SECTION F**

Contractor in process of making repairs at damaged framing.

PHOTOGRAPH #22



**BUILDING 26
SECTION G**

Contractor in process of making repairs at damaged breezeway built up beams and columns.
