

**PHOTOGRAPHS**

**PHOTOGRAPH #1**



**BUILDING 26  
SECTION A**

Breezeway steps and railing finish paint has been applied.

**PHOTOGRAPH #2**



**BUILDING 26  
SECTION A**

Entrance doors and sign finish paint has been applied.

**PHOTOGRAPH #3**



**BUILDING 26  
SECTION D**

Contractor has applied finish paint and is removing scaffolding.

**PHOTOGRAPH #4**



**BUILDING 26  
SECTION F**

Contractor has removed and repositioned dryer vents as directed.

**PHOTOGRAPH #5**



**BUILDING 26  
SECTION G**

Stucco sub-contractor applying brown coat of stucco.

**PHOTOGRAPH #6**



**BUILDING 26  
SECTION B**

Contractor installing repainted railings with 4" lag bolts set in sealant.

**PHOTOGRAPH #7**



**BUILDING 26  
SECTION B**

Contractor installing repainted railings with 4" lag bolts set in sealant.

**PHOTOGRAPH #8**



**BUILDING 26  
SECTION E**

Contractor spray painting new soffit with Sherwin Williams Legacy Ultra Prime.


**PHOTOGRAPH #9**



**BUILDING 26  
SECTION E**

Contractor spray painting new soffit with Florida Paints Legacy Ultra Prime

**PHOTOGRAPH #10**

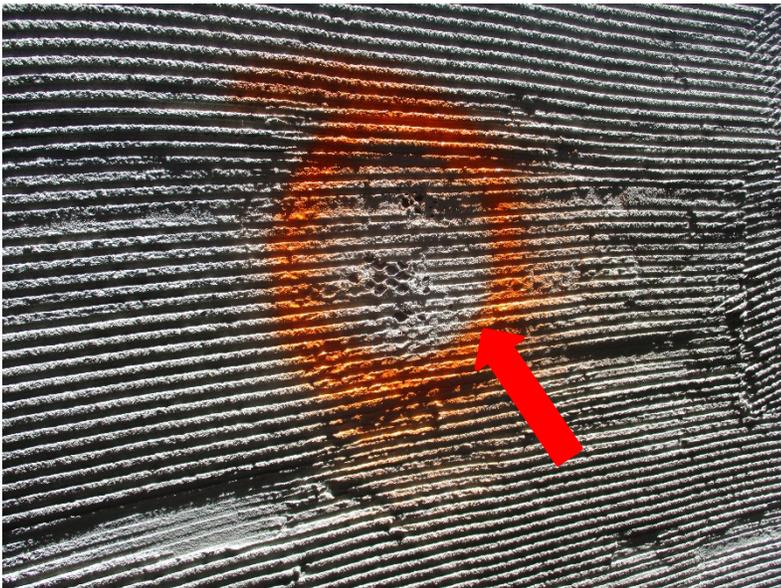

**BUILDING 27  
SECTION H**

Several areas of stucco scratch coat not properly embedded into metal lath have been marked for correction.

**PHOTOGRAPH #11**



**BUILDING 27  
SECTION H**

Stucco sub – contractor has made corrections at marked areas where scratch coat was deficient.

**PHOTOGRAPH #12**



**BUILDING 27  
SECTION G**

Flashing at unit # 2722 does not extend to the end of the new wall repairs and marked for corrections.

**PHOTOGRAPH #13**



**BUILDING 27  
SECTION G**

Contractor has made corrections at unit #2722 flashing deficiencies.

**PHOTOGRAPH #14**



**BUILDINGS 27  
SECTION F**

Contractor will be required to seal Tyvek WRB around AC electrical boxes before secondary WRB is applied by Stucco sub - contractor.

**PHOTOGRAPH #15**



**BUILDINGS 27  
SECTION F**

Contractor has completed Tyvek WRB, Dupont flashings and window installations.

**PHOTOGRAPH #16**



**BUILDINGS 27  
SECTION E**

Framing, strapping and Simpson Strong Tie connectors inspected for compliance.

**PHOTOGRAPH #17**



**BUILDINGS 27  
SECTION E**

Bora-Care termite treatment has been applied, insulation placed and ply-wood sheathing has begun.

**PHOTOGRAPH #18**



**BUILDINGS 27  
SECTION D**

Gable end framing repairs, strapping, Simpson Strong Tie connectors and termite treatment applied.

**PHOTOGRAPH #19**



**BUILDINGS 27  
SECTION C**

Framing damage inspected and marked for repairs.

**PHOTOGRAPH #20**



**BUILDINGS 27  
SECTION C**

Framing damage inspected and marked for repairs.


**PHOTOGRAPH #21**



**BUILDINGS 27  
SECTION C**

Framing damage inspected and marked for repairs.

**PHOTOGRAPH #22**

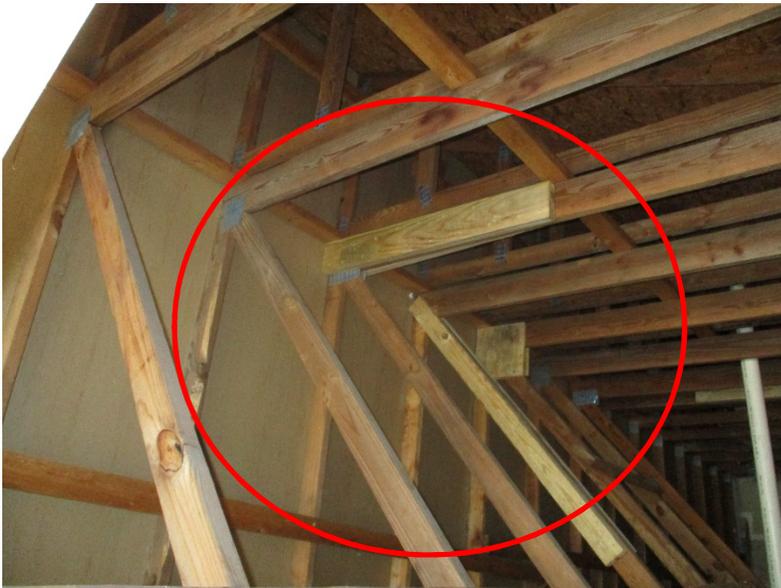

**BUILDINGS 27  
ATTIC #2728**

Repairs made to gussets, trusses and fire walls.

**PHOTOGRAPH #23**



**BUILDINGS 27  
ATTIC #2727**

Repairs made to gussets, trusses and fire walls.

**PHOTOGRAPH #24**



**BUILDINGS 27  
ATTIC #2727**

Repairs made to gussets, trusses and fire walls.
