

PHOTOGRAPHS

PHOTOGRAPH #1



**BUILDING 24
UNIT #2726**

New railing and screen enclosure are complete at balcony.

PHOTOGRAPH #2



**BUILDING 26
SECTION A**

Materials at stucco staging area have been removed.

PHOTOGRAPH #3



**BUILDING 26
SECTION B**

Contractor has begun to install new screen enclosures at ground level units.


PHOTOGRAPH #4



**BUILDING 26
SECTION C**

Contractor has installed several balcony railings and attached to walls with angles welded to railing top rail.

PHOTOGRAPH #5

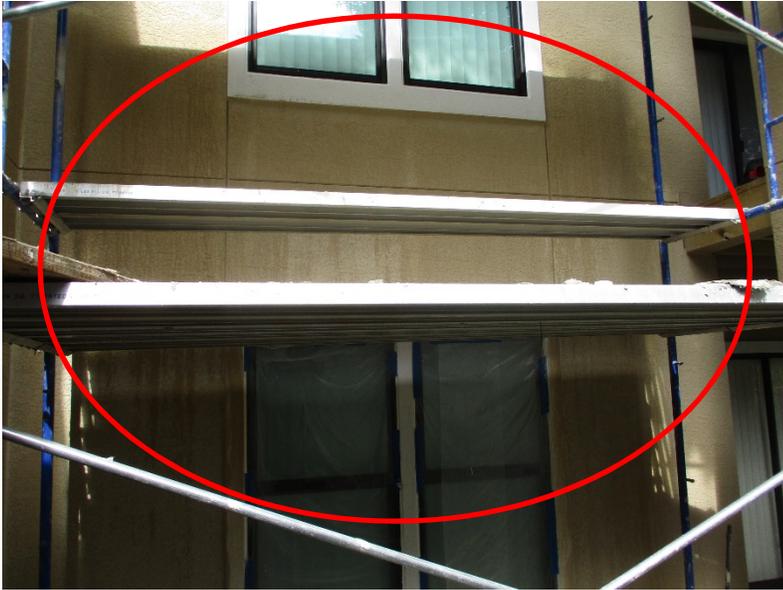

**BUILDING 26
SECTION F**

Finish coat of paint on stucco has washed off from rain and will require reapplication.

PHOTOGRAPH #6



**BUILDING 26
SECTION F**

Finish coat of paint on stucco has washed off from rain and will require reapplication.


PHOTOGRAPH #7



**BUILDING 26
SECTION G**

Sub-contractor has completed finish coat of stucco.

PHOTOGRAPH #8

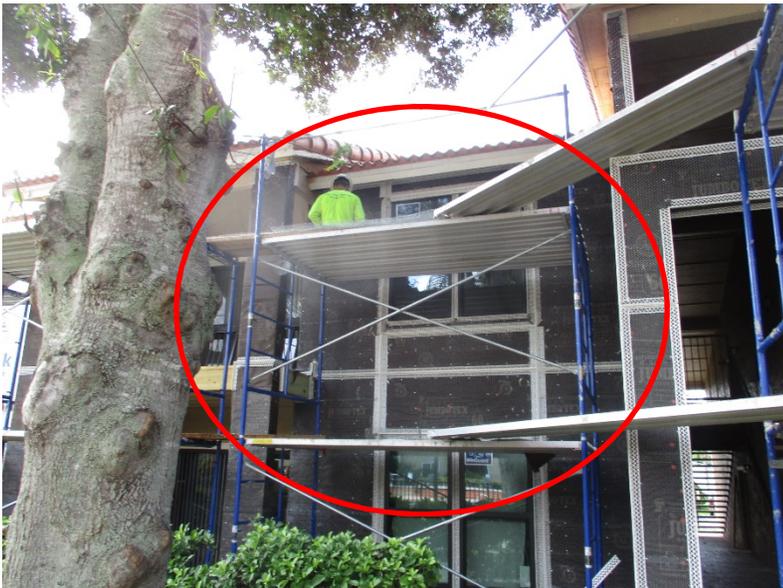

**BUILDING 2
SECTION G**

Stucco sub-contractor applying stucco accessories and metal lath.

PHOTOGRAPH #9



**BUILDING 26
SECTION G**

Stucco sub-contractor has installed alternate metal lath in this area that has not been submitted or approved for application.

PHOTOGRAPH #10



**BUILDING 27
SECTION H**

Stucco sub-contractor has installed alternate metal lath in this area that has not been submitted or approved for application.

PHOTOGRAPH #11



**BUILDING 27
SECTION E**

Plywood sheathing installed and inspected, is ready for Tyvek WRB and window installations.

PHOTOGRAPH #12



**BUILDING 27
SECTION D**

Contractor has begun to install plywood sheathing.

PHOTOGRAPH #13



**BUILDING 27
SECTION C**

Breezeway built up beams and framing damage, documented and marked for replacement.

PHOTOGRAPH #14



**BUILDING 27
SECTION C**

Breezeway built up beams and framing damage, documented and marked for replacement.

PHOTOGRAPH #15



**BUILDINGS 27
UNIT #2724**

Windows installations have been inspected for compliance.

PHOTOGRAPH #16



**BUILDINGS 27
UNIT #2724**

Windows installations have been inspected for compliance.

PHOTOGRAPH #17



**BUILDINGS 27
UNIT #2724**

Windows installations have been inspected for compliance.

PHOTOGRAPH #18



**BUILDINGS 27
UNIT #2724**

Windows installations have been inspected for compliance.

PHOTOGRAPH #19



**BUILDINGS 27
UNIT #2726**

Contractor has made drywall repairs at newly installed windows.

PHOTOGRAPH #20



**BUILDINGS 27
UNIT #2726**

Contractor has made drywall repairs at newly installed windows.
