

PHOTOGRAPHS

PHOTOGRAPH #1



BUILDING 26 SECTION E

Finish coat of paint has been re-applied at locations previously washed off.

PHOTOGRAPH #2



BUILDING 26 SECTION F

Finish coat of paint has been re-applied at locations previously washed off.

PHOTOGRAPH #3



**BUILDING 26
SECTION G**

Contractor has applied finish coating to stucco surfaces.

PHOTOGRAPH #4



**BUILDING 26
SECTION E**

Contractor is painting stair pads and stair railings.

PHOTOGRAPH #5



**BUILDING 26
UNIT # 2612**

Delta walked through all accessible units for inspection of interior window repair work with contractor and representative from Vintage Grand.

PHOTOGRAPH #6



**BUILDING 26
UNIT #2622**

Delta walked through all accessible units for inspection of interior window repair work with contractor and representative from Vintage Grand.

PHOTOGRAPH #7



**BUILDING 26
UNIT #2616**

Drywall has been damaged at interior side and contractor has scheduled repairs with owners.

PHOTOGRAPH #8



**BUILDING 26
UNIT #2616**

Contractor has spilled paint at tile area and has scheduled clean up with owners.

PHOTOGRAPH #9



**BUILDING 26
UNIT #2627**

Window does not open or close properly
and will be repaired by contractor.

PHOTOGRAPH #10



**BUILDING 27
SECTION G**

Stucco sub-contractor has applied finish
stucco.

PHOTOGRAPH #11



**BUILDING 27
SECTION F**

Stucco sub-contractor has installed alternate metal lath in this area that was not submitted or approved for application.

PHOTOGRAPH #12



**BUILDING 27
SECTION F**

Contractor has installed originally submitted and approved metal lath.

PHOTOGRAPH #13



**BUILDING 27
SECTION F**

Contractor has sealed Tyvek WRB around electrical boxes prior to application of secondary WRB applied by stucco sub-contractor.

PHOTOGRAPH #14



**BUILDING 27
SECTION F**

JobTex WRB has been applied by stucco sub-contractor.

PHOTOGRAPH #15



**BUILDING 27
SECTION E**

Weep screed stucco accessory being installed at base of new pressure treated plywood sheathing with sealant as required.


PHOTOGRAPH #16



**BUILDING 27
SECTION D**

Plywood sheathing installed and inspected for compliance.

PHOTOGRAPH #17

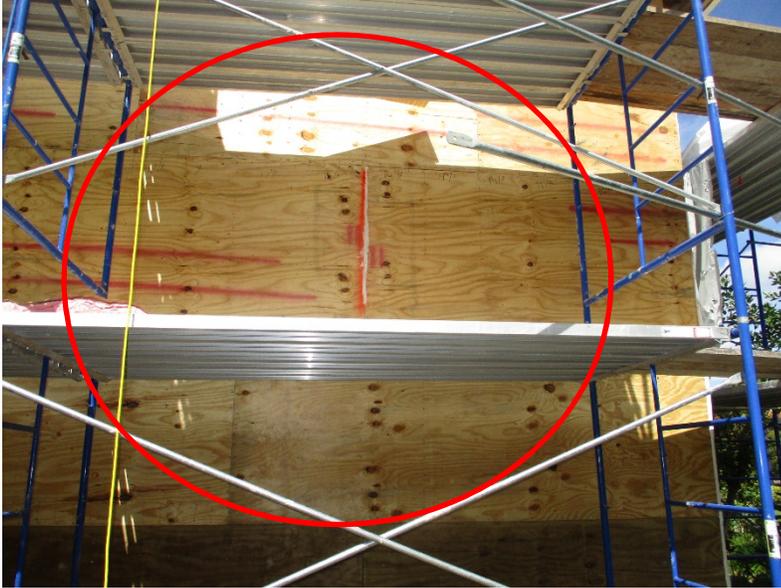

**BUILDING 27
SECTION D**

Contractor has made corrections at plywood installation marked by Delta.

PHOTOGRAPH #18



**BUILDING 27
SECTION D**

Tyvek WRB has been applied and new windows set into openings with Dupont flashings.

PHOTOGRAPH #19



**BUILDING 27
SECTION C**

Contractor has begun framing repairs at walls and subfloor areas.

PHOTOGRAPH #20



**BUILDINGS 27
SECTION A**

Contractor has erected access scaffolding and begun demolition.
