

PHOTOGRAPHS

PHOTOGRAPH #1



**BUILDING 27
SECTION F**

Contractor is installing window perimeter sealants.

PHOTOGRAPH #2



**BUILDING 27
SECTION F**

Stucco has been damaged beyond stucco stop vinyl accessory.

PHOTOGRAPH #3



**BUILDING 27
SECTION F**

New wood soffit and soffit vent has been installed and prepared for paint primer.


PHOTOGRAPH #4



**BUILDING 27
SECTION F**

Stucco Sub-contractor is applying sand coats and finish coats.

PHOTOGRAPH #5

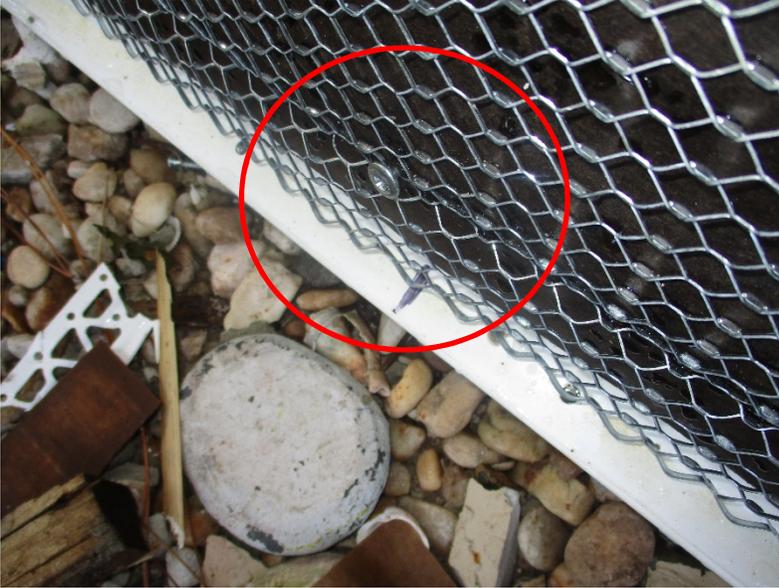

**BUILDING 27
SECTION E**

Metal lath fasteners were not properly installed.

PHOTOGRAPH #6



**BUILDING 27
SECTION E**

Stucco subcontractor corrected metal lath fasteners as directed.

PHOTOGRAPH #7



**BUILDING 27
SECTION D**

JumboTex WRB and stucco accessories are being installed.

PHOTOGRAPH #8



**BUILDING 27
SECTION C**

Tyvek WRB and Dupont flashing details applied and PGT windows installed.


PHOTOGRAPH #9



**BUILDING 27
SECTION B**

Contractor has applied plywood sheathing.

PHOTOGRAPH #10

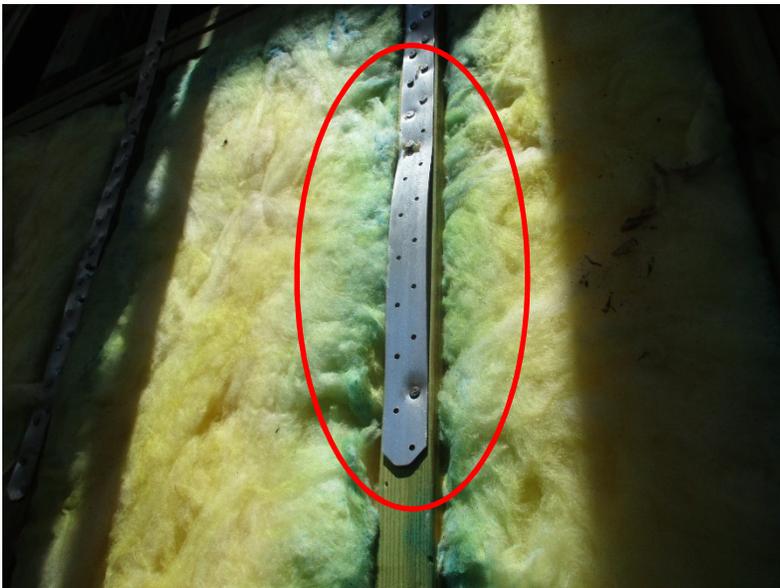

**BUILDING 27
SECTION B**

Simpson Strong-Tie connector strap has not been fully nailed. Contractor made corrections when discovered.

PHOTOGRAPH #11



**BUILDING 27
SECTION A**

Contractor has made full repairs at breezeway columns and built up beam.

PHOTOGRAPH #12



**BUILDING 27
SECTION D**

Unit #2727- ITA testing company water tested bedroom double windows following ASTM test methods and AAMA 502 testing guidelines outlined in project manual. Test failed with water intrusion at lower sill.

PHOTOGRAPH #13



**BUILDING 27
SECTION D**

Unit #2727- ITA testing company water tested bedroom double windows following ASTM test methods and AAMA 502 testing guidelines outlined in project manual. Test failed with water intrusion at lower sill.

PHOTOGRAPH #14



**BUILDING 27
SECTION D**

Unit #2727- ITA testing company water tested bedroom double windows following ASTM test methods and AAMA 502 testing guidelines outlined in project manual. Test failed with water intrusion at lower sill.

PHOTOGRAPH #15



**BUILDING 27
SECTION E**

Unit #2727- ITA testing company water tested 2nd bedroom double windows following ASTM test methods and AAMA 502 testing guidelines outlined in project manual. Test failed with water intrusion at lower sill.

PHOTOGRAPH #16



**BUILDING 27
SECTION D**

Unit #2727- ITA testing company water tested 2nd bedroom double windows following ASTM test methods and AAMA 502 testing guidelines outlined in project manual. Test failed with water intrusion at lower sill.

PHOTOGRAPH #17



**BUILDING 27
SECTION D**

Unit #2727- ITA testing company water tested 2nd bedroom double windows following ASTM test methods and AAMA 502 testing guidelines outlined in project manual. Test failed with water intrusion at lower sill.

PHOTOGRAPH #18



**BUILDING 10
SECTION D**

Contractor has erected access framing scaffolding.

PHOTOGRAPH #19



**BUILDING 10
SECTION F**

Contractor has erected access framing scaffolding.
