

## PHOTOGRAPHS

**PHOTOGRAPH #1**



### **BUILDING 27 SECTION F**

Contractor has applied finish paint at stucco and wood trim.

**PHOTOGRAPH #2**



### **BUILDING 27 SECTION F**

Stucco has been repaired where damaged beyond stucco stop vinyl accessory.

**PHOTOGRAPH #3**



**BUILDING 27  
SECTION F**

At several balconies flashing has not been properly sealed at transition to stucco accessories.

**PHOTOGRAPH #4**



**BUILDING 27  
SECTION F**

At several balconies flashing has not been properly sealed at transition to stucco accessories.

**PHOTOGRAPH #5**



**BUILDING 27  
SECTION F**

Kick out flashing is not lapped or sealed properly.

**PHOTOGRAPH #6**



**BUILDING 27  
SECTION E**

Stucco subcontractor is applying sand and finish coats of stucco.

**PHOTOGRAPH #7**



**BUILDING 27  
SECTION D**

JumboTex WRB and stucco accessories are being installed.

**PHOTOGRAPH #8**



**BUILDING 27  
SECTION C**

JumboTex WRB is being installed.

**PHOTOGRAPH #9**



**BUILDING 27  
SECTION A**

Gaps between sheets of plywood sheathing at several window head locations are not 1/8".

**PHOTOGRAPH #10**



**BUILDING 27  
SECTION A**

PT plywood has been sealed to concrete slab per C.O. # 2.


**PHOTOGRAPH #11**



**BUILDING 27  
SECTION A**

Contractor installing plywood sheathing.

**PHOTOGRAPH #12**

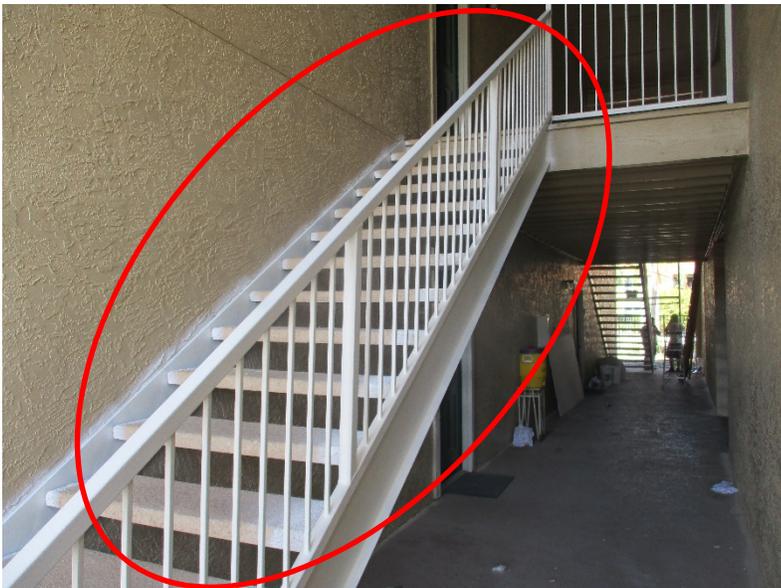

**BUILDING 27  
SECTION A- BREEWAY**

Contractor has primed steel at stairs and railings with Florida Paints Epoxy Mastic Primer.

**PHOTOGRAPH #13**



**BUILDING 10  
SECTION E AND F**

Contractor has erected frame scaffold and provided construction fencing.
