

**PHOTOGRAPHS**

**PHOTOGRAPH #1**



**BUILDING 10  
SECTION E-BREEZWAY**

Contractor removing paint and rust from railings in preparation for priming and finish painting.

**PHOTOGRAPH #2**



**BUILDING 10  
SECTION E-BREEZWAY**

Contractor removing paint and rust from railings in preparation for priming and finish painting.

**PHOTOGRAPH #3**



**BUILDING 10  
SECTION E – UNIT #1028**

Contractor refinishing drywall at new window installation.

**PHOTOGRAPH #4**



**BUILDING 10  
SECTION E – UNIT #1028**

Window opening flashed with DuPont flashing and interior sealant installed.

**PHOTOGRAPH #5**



**BUILDING 10  
SECTION F**

Stucco sub-contractor applying scratch coat of stucco.

**PHOTOGRAPH #6**



**BUILDING 10  
SECTION G**

Water resistant barrier, stucco accessories and lath in place and ready for stucco application.

**PHOTOGRAPH #7**



**BUILDING 10  
SECTION G**

Corner of stucco accessories missing required sealant. Contractor notified.

**PHOTOGRAPH #8**



**BUILDING 10  
SECTION G**

Sub-contractor made corrections by applying sealant at accessory transition.

**PHOTOGRAPH #9**



**BUILDING 10  
SECTION G- BREEZWAY**

Steel railing picket has broken loose where deteriorated.


**PHOTOGRAPH #10**



**BUILDING 10  
SECTION H**

Sub-contractor has applied JumboTex 60 and in process of installing stucco accessories.

**PHOTOGRAPH #11**

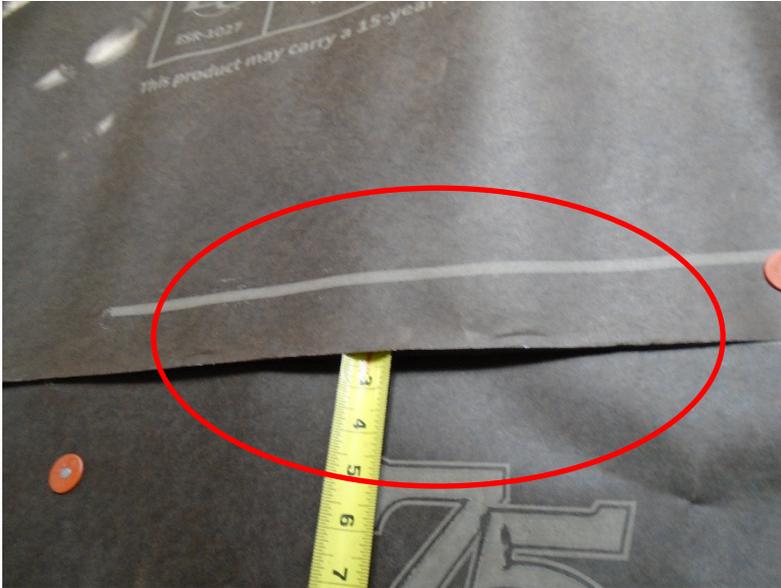

**BUILDING 10  
SECTION H**

JumboTex 60 WRB overlapped as per manufacturers installation instructions.

**PHOTOGRAPH #12**



**BUILDING 10  
SECTION A**

Contractor has made repairs at damaged window framing.

**PHOTOGRAPH #13**



**BUILDING 10  
SECTION A**

Contractor installing Simpson Strong-Tie straps and connectors.

**PHOTOGRAPH #14**



**BUILDING 10  
SECTION B**

Contractor performing framing repairs at triple window.

**PHOTOGRAPH #15**



**BUILDING 10  
SECTION B**

Contractor using 16d common nails for framing repairs.

**PHOTOGRAPH #16**



**BUILDING 10  
SECTION B**

Contractor has installed Simpson Strong-Tie straps and connectors.


**PHOTOGRAPH #17**



**BUILDING 10  
SECTION B**

Contractor has made window header repairs at triple window.

**PHOTOGRAPH #18**

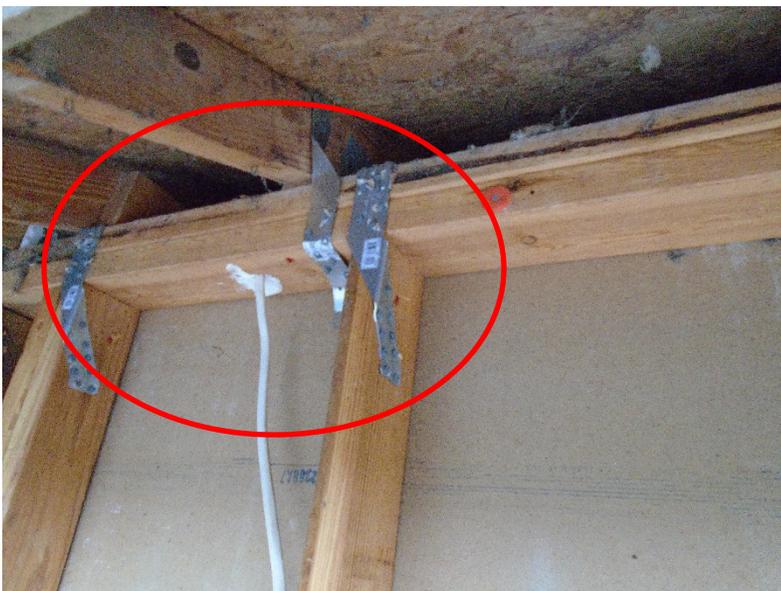

**BUILDING 10  
SECTION B**

Simpson Strong-Tie connectors and screws have been installed at top plate and truss connections.
