


## PHOTOGRAPHS

**PHOTOGRAPH #1**

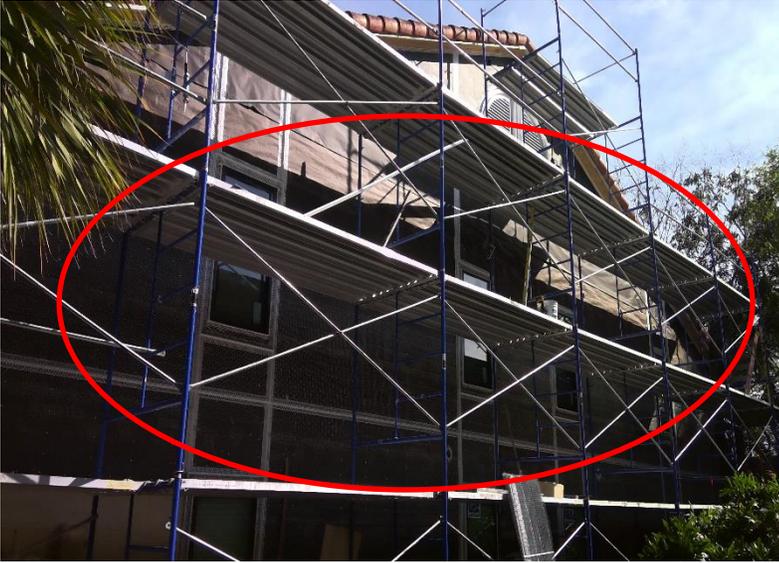

### **BUILDING 5 SECTION D**

Stucco Sub contractor applying lath for stucco application.

**PHOTOGRAPH #2**



### **BUILDING 5 SECTION D**

Louvered vents installed and flashed into wall system with Dupont flexwrap flashing.

**PHOTOGRAPH #3**



**BUILDING 5  
SECTION E**

New PGT windows installed and stucco accessories with wire lath in place for stucco applications.

**PHOTOGRAPH #4**



**BUILDING 5  
SECTION F**

New galvanized kick out flashing details installed at balconies with stucco accessories and wire lath in place for stucco applications.

**PHOTOGRAPH #5**



**BUILDING 5  
SECTION F**

Galvanized kick out flashing detail installed over new PT decking boards.

**PHOTOGRAPH #6**



**BUILDING 5  
SECTION H**

Contractor has applied new 15/32" plywood sheathing.

**PHOTOGRAPH #7**



**BUILDING 5  
SECTION H**

Contractor has applied Tyvek HomeWrap WRB for dry in of wall and begun installation of window flashing.

**PHOTOGRAPH #8**



**BUILDING 5  
SECTION H**

Contractor has begun applying Dupont flashing at window openings and installation of PGT windows.

**PHOTOGRAPH #9**



**BUILDING 5  
SECTION A**

Balcony and wall framing repairs in progress where identified and marked by Delta.

**PHOTOGRAPH #10**



**BUILDING 5  
SECTION A**

Full breezeway framing repairs performed and strapping in place.

**PHOTOGRAPH #11**



**BUILDING 5  
SECTION B**

Balcony and wall framing repairs in progress where identified and marked by Delta.

**PHOTOGRAPH #12**



**BUILDING 5  
SECTION B**

Balcony and wall framing repairs in progress where identified and marked by Delta.

**PHOTOGRAPH #13**



**BUILDING 5  
SECTION B**

New pressure treated lumber for decking flooring replacement.
