

PHOTOGRAPHS

PHOTOGRAPH #1



BUILDING 5 SECTION D

Florida Paints primer and finish Acrylic paint has been applied to new stucco.

PHOTOGRAPH #2



BUILDING 5 SECTION E

Florida Paints primer and finish Acrylic paint has been applied to new stucco.

PHOTOGRAPH #3



**BUILDING 5
SECTION E**

Florida Paints primer and finish Acrylic paint has been applied to new stucco.

PHOTOGRAPH #4



**BUILDING 5
SECTION F**

New BASF sealant are being applied at all inside corner transitions prior to painting.


PHOTOGRAPH #5



**BUILDING 5
SECTION G**

Stucco Sub-contractor has applied new finish coats of stucco.

PHOTOGRAPH #6

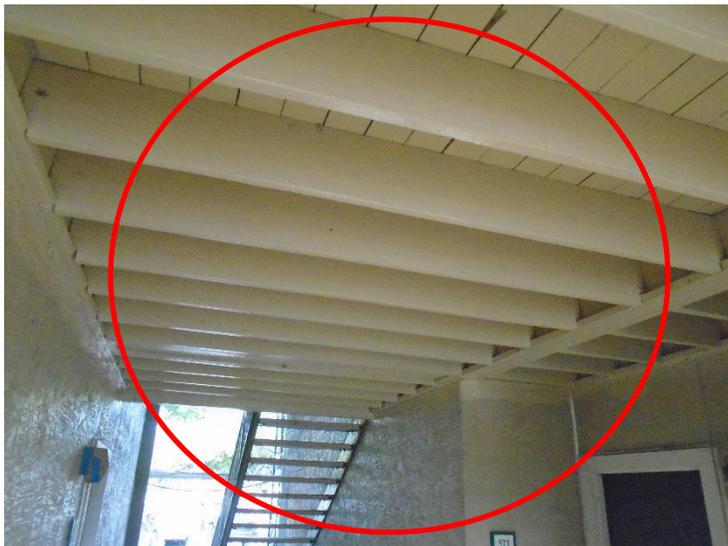

**BUILDING 5
SECTION G - BREEZEWAY**

Florida Paints primer and finish Acrylic paint has been applied to previously painted wood and stucco.

PHOTOGRAPH #7



**BUILDING 5
SECTION H**

Stucco sub-contractor has applied new three coat system of scratch, brown and finish stucco.

PHOTOGRAPH #8



**BUILDING 5
SECTION A**

Stucco sub-contractor has applied new scratch and brown coats of stucco.

PHOTOGRAPH #9



**BUILDING 5
SECTION B**

Stucco sub-contractor has applied new scratch coat of stucco.

PHOTOGRAPH #10



**BUILDING 5
SECTION C**

Stucco sub-contractor in process of applying JumboTex WRB, stucco accessories and metal lath in preparation for new stucco.

PHOTOGRAPH #11



**BUILDING 5
SECTION C**

New wood soffit and soffit screening has been installed.

PHOTOGRAPH #12



**BUILDING 5
SECTION C**

Gap in soffit trim will be filled at transition with new sealant prior to finish painting.

PHOTOGRAPH #13



**BUILDING 23
SECTION H**

Delta marked missing fasteners at perimeter sheathing. Corrections made by Contractor.

PHOTOGRAPH #14



**BUILDING 23
SECTION H**

Delta marked gaps at sheathing. Corrections made by contractor.

PHOTOGRAPH #15



**BUILDING 23
SECTION H**

Contractor in process of applying new Tyvek HomeWrap WRB over new plywood sheathing.

PHOTOGRAPH #16



**BUILDING 23
SECTION G**

Delta marked missing fasteners at perimeter sheathing. Corrections made by Contractor.

PHOTOGRAPH #17



**BUILDING 23
SECTION G**

Delta marked missing fasteners at perimeter sheathing. Corrections made by Contractor.

PHOTOGRAPH #18



**BUILDING 23
SECTION F**

Contractor in process of installing Simpson Strong-Tie framing connectors and strapping at wall framing.

PHOTOGRAPH #19



**BUILDING 23
SECTION F**

Contractor performing full balcony and deck board replacement repairs at both balcony decks.

PHOTOGRAPH #20



**BUILDING 23
SECTION E- BREEZEWAY**

Extensive termite damage to wood framing at breezeway return walls and subflooring.

PHOTOGRAPH #21



**BUILDING 23
SECTION E -BREEZEWAY**

Contractor has made repairs to breezeway framing damage and subflooring.

PHOTOGRAPH #22



**BUILDING 23
SECTION E**

Contractor in process of balcony railing preparation for painting.
