

**PHOTOGRAPHS**

**PHOTOGRAPH #1**



**BUILDING 23  
SECTION H**

Stucco Sub-contractor applying scratch coat of stucco.

**PHOTOGRAPH #2**



**BUILDING 23  
SECTION H**

Stucco Sub-contractor applying brown coat of stucco.

**PHOTOGRAPH #3**



**BUILDING 23  
SECTION G**

Stucco Sub-contractor has applied  
scratch coat of stucco.

**PHOTOGRAPH #4**



**BUILDING 23  
SECTION F**

Stucco Sub-contractor has applied  
scratch coat of stucco.

**PHOTOGRAPH #5**



**BUILDING 23  
SECTION F**

Scratch coat of stucco washed out in this section and will require corrections.

**PHOTOGRAPH #6**



**BUILDING 23  
SECTION F**

Stucco Sub – contractor has corrected section of washed out scratch coat as directed.

**PHOTOGRAPH #7**



**BUILDING 23  
SECTION E**

Voids at the accessories and lath will require corrections as marked by Delta.

**PHOTOGRAPH #8**



**BUILDING 23  
SECTION E**

Stucco Sub – contractor has corrected areas of voids as directed by Delta.

**PHOTOGRAPH #9**



**BUILDING 23  
SECTION D**

Stucco contractor applied stucco accessories and metal lathing in preparation for stucco applications.

**PHOTOGRAPH #10**



**BUILDING 23  
SECTION C**

JumboTex Water Resistant Barrier in place and stucco accessory applications in progress.


**PHOTOGRAPH #11**



**BUILDING 23  
SECTION B**

JumboTex Water Resistant Barrier in place and stucco accessory applications in progress.

**PHOTOGRAPH #12**

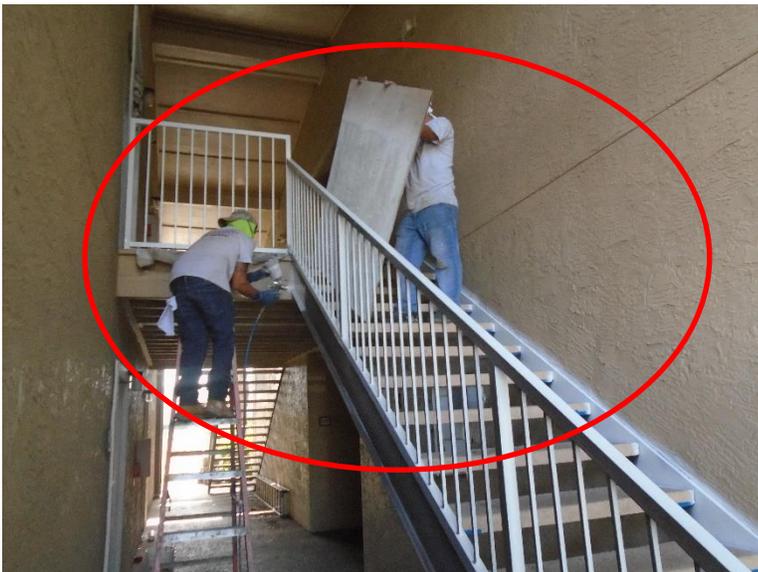

**BUILDING 23  
SECTION B**

Contractor spray priming stairway railings with Florida Paints Encapsulant epoxy mastic primer.

**PHOTOGRAPH #13**



**BUILDING 23  
SECTION B**

Contractor spray priming stairway railings with Florida Paints Encapsulant epoxy mastic primer.

**PHOTOGRAPH #14**



**BUILDING 21  
SECTION H**

Contractor has performed framing repairs, gable end reinforcement, strapping and Simpson Strong -Tie connectors.

**PHOTOGRAPH #15**



**BUILDING 21  
SECTION H**

Contractor has performed framing repairs, gable end reinforcement, strapping and Simpson Strong -Tie connectors.

**PHOTOGRAPH #16**



**BUILDING 21  
SECTION H**

Attic framing repairs in progress.

**PHOTOGRAPH #17**



**BUILDING 21  
SECTION G**

Termite damage at top plate at **Unit #2112** is extensive and may extend into owners Unit.

**PHOTOGRAPH #18**



**BUILDING 21  
SECTION G**

Termite damage at top plate at **Unit #2112** is extensive and may extend into owners Unit.

**PHOTOGRAPH #19**



**BUILDING 21  
SECTION F**

Contractor has begun framing and balcony damage repairs.

**PHOTOGRAPH #20**



**BUILDING 21  
SECTION A**

Framing damage and collapse observed and documented.
