

PHOTOGRAPHS

PHOTOGRAPH #1



**BUILDING 5- UNIT 526
PUNCH LIST**

Living room- middle operable window is loose from frame.

PHOTOGRAPH #2



**BUILDING 5- UNIT 526
PUNCH LIST**

Balcony railing attachments have begun to show surface rust.

PHOTOGRAPH #3



**BUILDING 5- UNIT 528
PUNCH LIST**

Bedroom- Right operable window is loose from frame.

PHOTOGRAPH #4



**BUILDING 5- UNIT 527
PUNCH LIST**

Guest bedroom - WOCD safety device is broken.

PHOTOGRAPH #5



**BUILDING 5- UNIT 523
PUNCH LIST**

Guest bedroom - WOCD safety device is missing.

PHOTOGRAPH #6



**BUILDING 23
SECTION H**

Painting has been completed and scaffolding has been removed.

PHOTOGRAPH #7



**BUILDING 23
SECTION G**

Problematic tree roots at base of walls.

PHOTOGRAPH #8



**BUILDING 23
SECTION G**

Simpson Strong - Tie screws and clips had not been installed at rim joist. Delta notified contractor.


PHOTOGRAPH #9



**BUILDING 23
SECTION G**

Contractor has installed Simpson Strong – Tie screws and clips.

PHOTOGRAPH #10

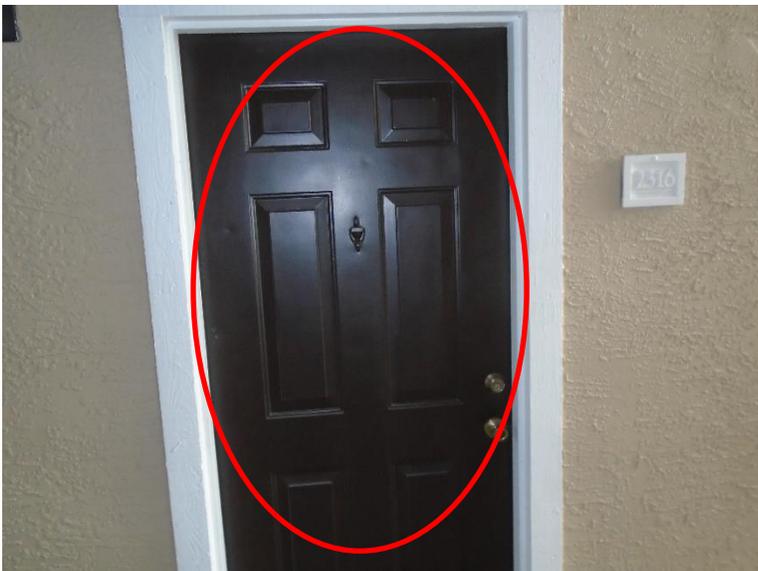

**BUILDING 23
SECTION G**

Florida Paint finish enamel has been applied to front doors.

PHOTOGRAPH #11



**BUILDING 23
SECTION F**

Contractor has completed painting of walls and in process of removing scaffolding.

PHOTOGRAPH #12



**BUILDING 23
SECTION E**

Caulking details at top of rim joist and cedar face trim have not been provided with urethane sealants.

PHOTOGRAPH #13



**BUILDING 23
SECTION D**

Contractor in process of priming new stucco with Florida Paints acrylic primer.

PHOTOGRAPH #14



**BUILDING 23
SECTION D**

Contractor in process of priming new stucco with Florida Paints acrylic primer.

PHOTOGRAPH #15



**BUILDING 23
SECTION C**

Steel railings showing surface rust after application of primer will require additional preparation and re priming before finish coat of paint.

PHOTOGRAPH #16



**BUILDING 23
SECTION C**

Steel railings showing surface rust after application of primer will require additional preparation and re priming before finish coat of paint.

PHOTOGRAPH #17



**BUILDING 23
SECTION A**

Stucco sub-contractor applying texture coat of stucco.

PHOTOGRAPH #17



**BUILDING 23
SECTION A**

Stucco sub-contractor applying texture coat of stucco.

PHOTOGRAPH #17



**BUILDING 23
SECTION A**

Stucco sub-contractor applying texture coat of stucco.

PHOTOGRAPH #18



**BUILDING 21
SECTION H**

Sub- Contractor installing stucco accessories in preparation for lath and stucco.

PHOTOGRAPH #19



**BUILDING 21
SECTION G
UNIT 2121**

Contractor has supported bottom plate by forming and pouring BASF MasterEmaco N 425 under bottom plate.

PHOTOGRAPH #20



**BUILDING 21
SECTION G
UNIT 2121**

Contractor has supported bottom plate by forming and pouring BASF MasterEmaco N 425 under bottom plate.

PHOTOGRAPH #21



**BUILDING 21
SECTION F**

Deck framing repairs and new decking boards on balconies.

PHOTOGRAPH #22



**BUILDING 21
SECTION F**

Breezeway framing repairs complete and new sheathing installed.

PHOTOGRAPH #23



**BUILDING 21
SECTION F**

BoraCare termite treatment applied to framing.

PHOTOGRAPH #24



**BUILDING 21
SECTION E**

Simpson Strong – Tie straps, screws, and connectors in place at framing, window headers and roof trusses.
