

PHOTOGRAPHS

PHOTOGRAPH #1



**BUILDING 23
SECTION G**

Contractor has completed trim painting and re installed repainted balcony railing.

PHOTOGRAPH #2



**BUILDING 23
SECTION G**

Contractor has painted front doors, trim and unit signs.

PHOTOGRAPH #3



**BUILDING 23
SECTION G**

Stairway railing repairs have not been completed prior to finish painting.

PHOTOGRAPH #4



**BUILDING 23
SECTION F**

Contractor has completed trim painting and re installed repainted balcony railing.

PHOTOGRAPH #5



**BUILDING 23
SECTION E**

Stairway railing repairs have not been completed prior to finish painting

PHOTOGRAPH #6



**BUILDING 23
SECTION E**

Contractor has completed trim painting and re installed repainted balcony railing.

PHOTOGRAPH #7



**BUILDING 23
SECTION D**

Trim painting completed and dryer vents installed.

PHOTOGRAPH #8



**BUILDING 23
SECTION C**

Pickets and bottom rail welding repairs have begun at stairway railings.

PHOTOGRAPH #9



**BUILDING 23
SECTION C**

Contractor has installed new BASF 150 sealants at window perimeters and transition joints.

PHOTOGRAPH #10



**BUILDING 23
SECTION B**

Stucco completed and cedar trim installed at balcony facing.


PHOTOGRAPH #11



**BUILDING 23
SECTION A**

Stucco finish completed and new sealants installed at window perimeters and transition joints.

PHOTOGRAPH #12

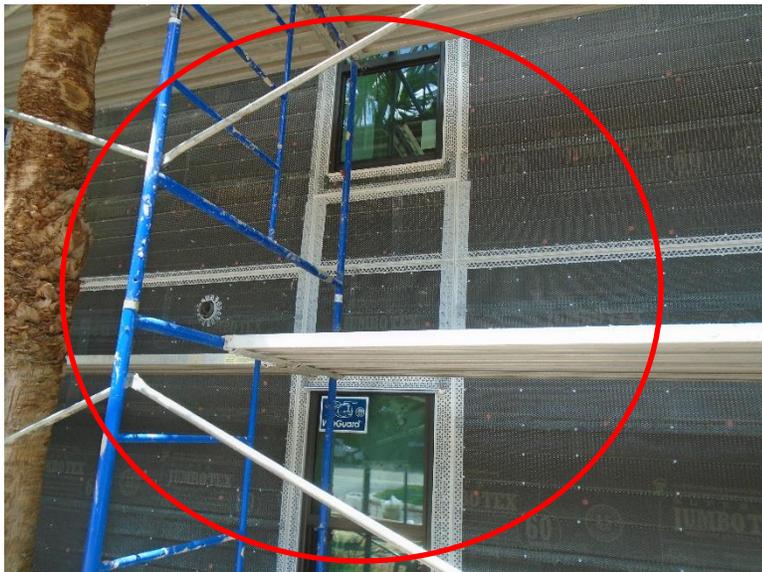

**BUILDING 21
SECTION H**

Stucco accessories and metal lath installed in compliance with ASTM C1063.

PHOTOGRAPH #13



**BUILDING 21
SECTION G**

Sub-contractor in process installing stucco accessories and metal lath.

PHOTOGRAPH #14



**BUILDING 21
SECTION G**

Contractor has applied Tyvek WRB and Dupont flashings prior to installation of new PGT windows.

PHOTOGRAPH #15



**BUILDING 21
SECTION F**

Contractor has applied Tyvek WRB and Dupont flashings prior to installation of new PGT windows.

PHOTOGRAPH #16



**BUILDING 21
SECTION D**

Contractor has begun stucco removal, exposing existing Thermo Ply product.

PHOTOGRAPH #17



**BUILDING 21
SECTION B**

Contractor has erected scaffolding for access to repairs and installed temporary construction fencing.
