

PHOTOGRAPHS

PHOTOGRAPH #1



BUILDING 21 SECTION F

Transition sealants being installed at inside corners are messy and will require professional tooling application.

PHOTOGRAPH #2



BUILDING 21 SECTION E- UNIT #2118

Interior window installation inspection confirms flashings and sealants in accordance with AAMA and manufacturer installation guidelines.


PHOTOGRAPH #3



**BUILDING 21
SECTION E- UNIT #2118**

Interior window installation inspection confirms flashings and sealants in accordance with AAMA and manufacturer installation guidelines.

PHOTOGRAPH #4

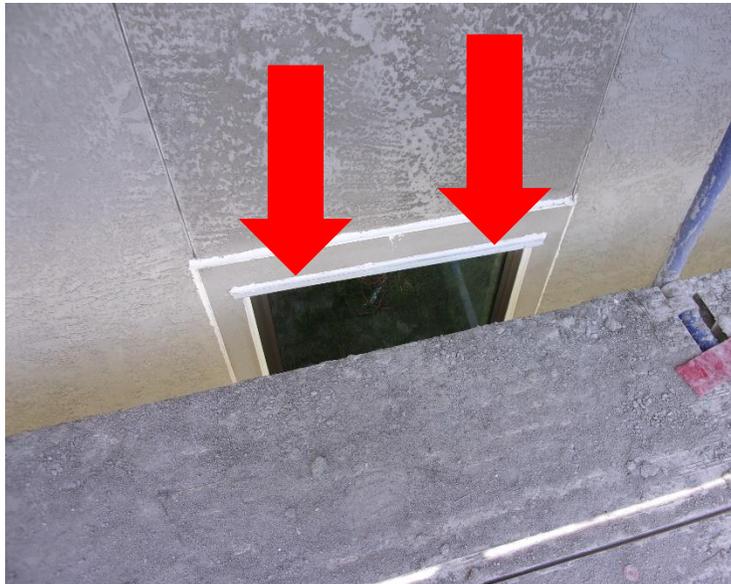

**BUILDING 21
SECTION D**

Contractor has sealed several windows' above head flashing not allowing open weep design and will be required to remove sealant.

PHOTOGRAPH #5



**BUILDING 21
SECTION C**

Soffits have been primed and contractor is sealing wood to wood transitions as well as fastener holes in preparation for finish coat of paint.

PHOTOGRAPH #6



**BUILDING 21
SECTION C**

Brown coat and finish coat of stucco has been applied.


PHOTOGRAPH #7



**BUILDING 21
SECTION B**

Stucco sub-contractor applying scratch coat of stucco.


PHOTOGRAPH #8

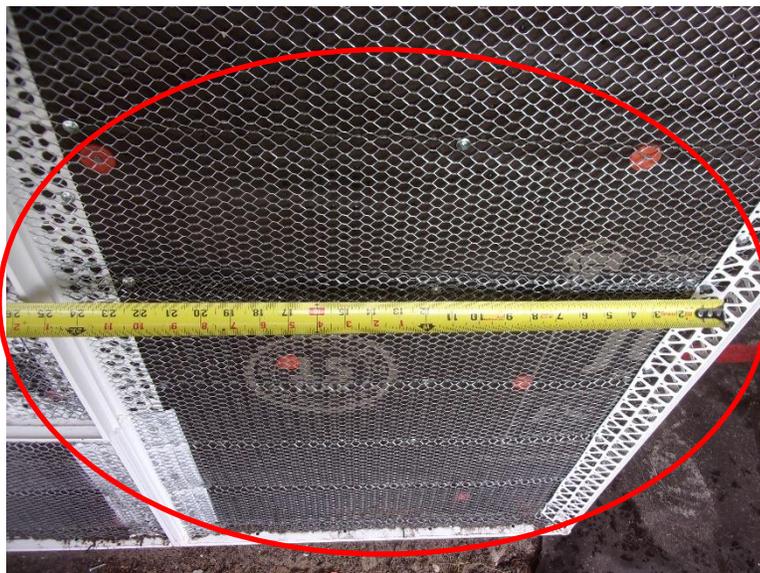

**BUILDING 21
SECTION A**

Lath and stucco accessories checked for correct fasteners, tie wires and lapping compliance.

PHOTOGRAPH #9

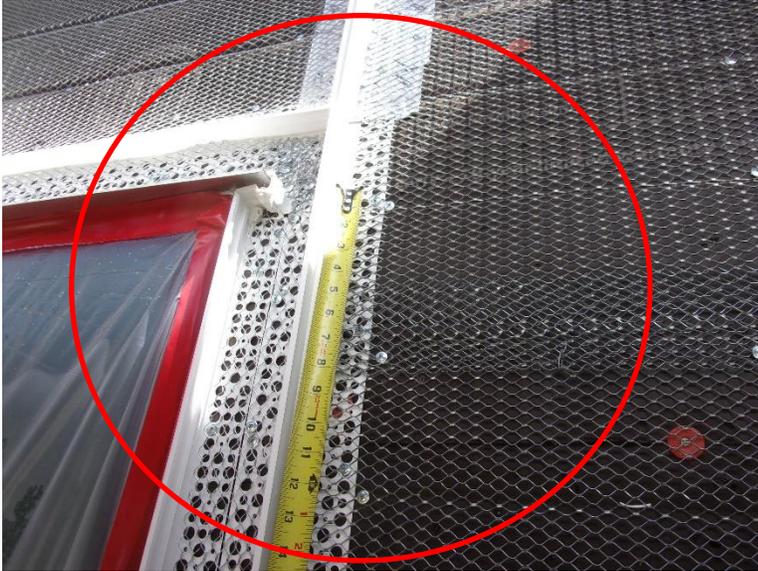

**BUILDING 21
SECTION A**

Lath and stucco accessories checked for correct fasteners, tie wires and lapping compliance.

PHOTOGRAPH #10



**BUILDING 21
SECTION A**

Scratch coat of stucco did not fill lath properly at several locations.

PHOTOGRAPH #11



**BUILDING 21
SECTION A**

Scratch coat of stucco did not fill lath properly at several locations.

PHOTOGRAPH #12



**BUILDING 21
SECTION A**

Stucco sub-contractor made corrections at scratch coat as directed by Delta.


PHOTOGRAPH #13



**BUILDING 20
SECTION H**

Simpson Strong-Tie strapping and termite treatment has been provided.

PHOTOGRAPH #14

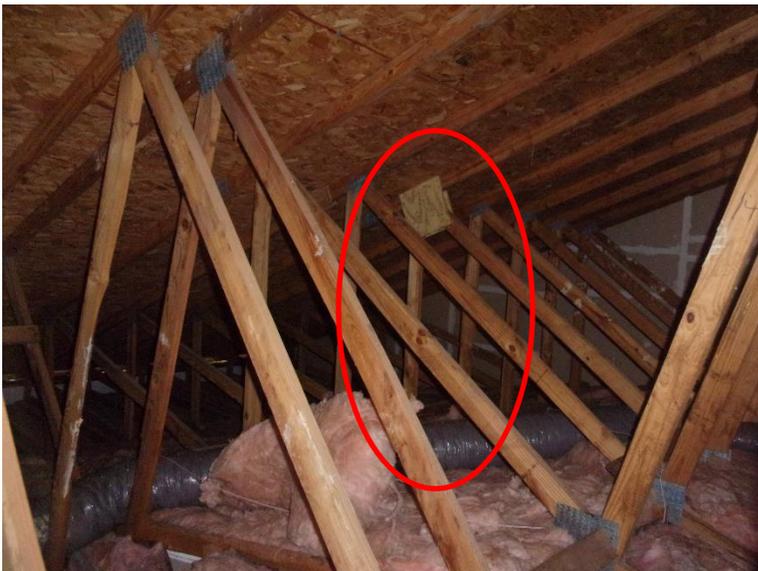

**BUILDING 20
SECTION H – ATTIC #2022**

Gussets, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #15



**BUILDING 20
SECTION H – ATTIC #2022**

Gussets, scabs, and fire wall repairs performed and quantified

PHOTOGRAPH #16



**BUILDING 20
SECTION H – ATTIC #2021**

Gussets, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #17



**BUILDING 20
SECTION H – ATTIC #2021**

Gussets, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #18



**BUILDING 20
SECTION A**

Balcony and breezeway framing repairs performed and quantified.

PHOTOGRAPH #19



**BUILDING 20
SECTION B**

Additional damage uncovered and repaired at patio storage door header and wall framing.

PHOTOGRAPH #20



**BUILDING 20
SECTION B**

Additional damage uncovered and repaired at patio storage door header and wall framing.

PHOTOGRAPH #21



**BUILDING 20
SECTION B**

Balcony framing and decking repaired and quantified.

PHOTOGRAPH #22



**BUILDING 20
SECTION C**

Damaged window opening framing repaired and quantified.
