

PHOTOGRAPHS

PHOTOGRAPH #1



BUILDING 21 SECTION G

Simpson Strong-Tie screws and clip hardware installed at balcony built up beams.

PHOTOGRAPH #2



BUILDING 21 SECTION G

Contractor painting stairway steps with Florida Paints concrete sealer.

PHOTOGRAPH #3



**BUILDING 21
SECTION G**

Contractor painting stairway steps with Florida Paints concrete sealer.

PHOTOGRAPH #4



**BUILDING 21
SECTION G- UNIT #2112**

Gaps at heads of 3 windows in bedroom area exceed maximum allowed gap for fastening of new PGT windows. Window will require corrective measures to meet manufacturer's NOA requirements.

PHOTOGRAPH #5



**BUILDING 21
SECTION G- UNIT #2112**

Gaps at heads of 3 windows in bedroom area exceed maximum allowed gap for fastening of new PGT windows. Window will require corrective measures to meet manufacturer's NOA requirements.

PHOTOGRAPH #6



**BUILDING 21
SECTION G- UNIT #2112**

Gaps at heads of 3 windows in bedroom area exceed maximum allowed gap for fastening of new PGT windows. Window will require corrective measures to meet manufacturer's NOA requirements.

PHOTOGRAPH #7



**BUILDING 21
SECTION B**

Several transition sealants are messy and will require correction with professional tooling application.

PHOTOGRAPH #8



**BUILDING 21
SECTION B**

Several transition sealants are messy and will require correction with professional tooling application.

PHOTOGRAPH #9



**BUILDING 21
SECTION B**

Contractor has filled gap above flashing with paint and will be required to remove.

PHOTOGRAPH #10



**BUILDING 21
SECTION B**

BASF manufacturer's representative tested and passed new sealants at window perimeters and will produce report for job files.

PHOTOGRAPH #11



**BUILDING 21
SECTION A**

Stucco painting has been completed and scaffolding is being removed.

PHOTOGRAPH #12



**BUILDING 21
SECTION G- UNIT #2111**

Windows inspected at unit interior for compliance with PGT NOA requirements and Dupont/ Tyvek flashing requirements.


PHOTOGRAPH #13



**BUILDING 21
SECTION G- UNIT #2111**

Windows inspected at unit interior for compliance with PGT NOA requirements and Dupont/ Tyvek flashing requirements.

PHOTOGRAPH #14

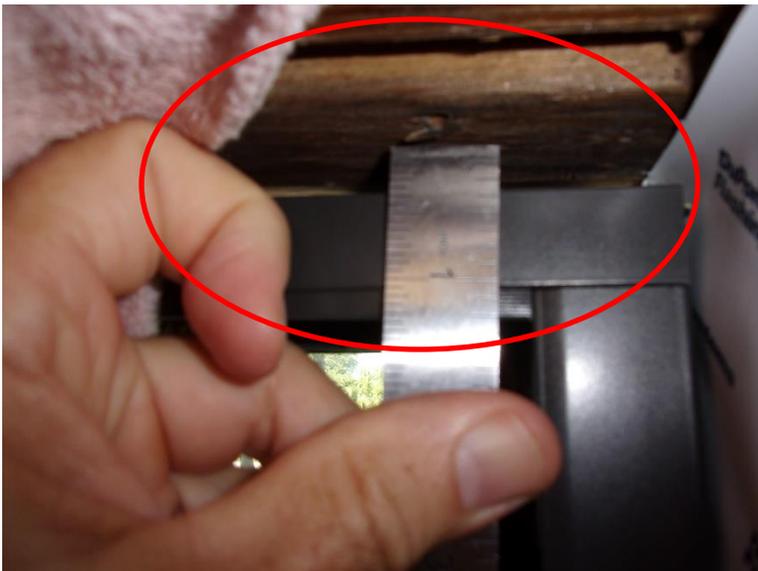

**BUILDING 21
SECTION G- UNIT #2111**

Windows inspected at unit interior for compliance with PGT NOA requirements and Dupont/ Tyvek flashing requirements.

PHOTOGRAPH #15



**BUILDING 20
SECTION A – UNIT #2011**

Contractor has fully covered open walls preventing any damage from exterior elements while waiting for windows to complete finish work.

PHOTOGRAPH #16



**BUILDING 20
SECTION A**

Contractor has fully covered open walls preventing any damage from exterior elements while waiting for windows to complete finish work.

PHOTOGRAPH #17



**BUILDING 20
SECTION B**

Contractor had failed to cover open walls and insulation at balcony return areas resulting in insulation damage.

PHOTOGRAPH #18



**BUILDING 20
SECTION B**

Contractor had failed to cover open walls and insulation at balcony return areas resulting in insulation damage

PHOTOGRAPH #19



**BUILDING 20
SECTION B**

Contractor fully covered and protected open walls at balcony return areas.

PHOTOGRAPH #20



**BUILDING 20
SECTION B**

New R-13 insulation installed where damaged or missing.


PHOTOGRAPH #21



**BUILDING 20
SECTION B**

Contractor installing plywood sheathing using pressure treated 15/32" at bottom sheet.

PHOTOGRAPH #22

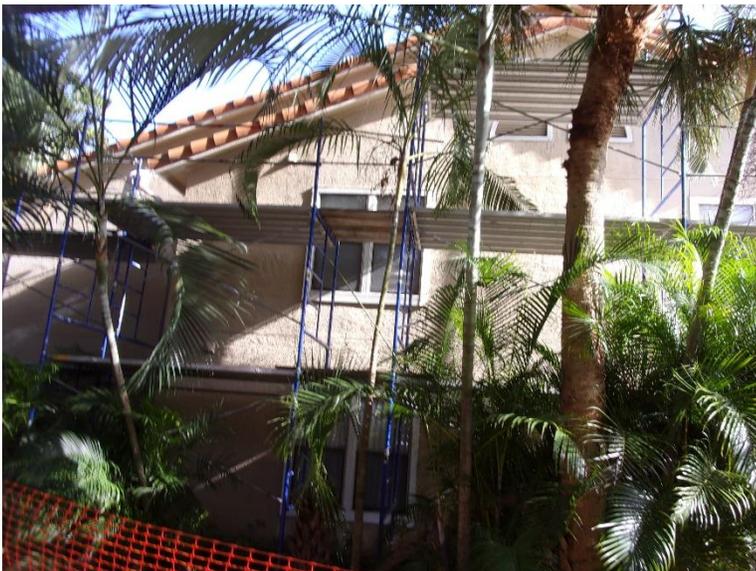

**BUILDING 20
SECTION D**

Scaffolding has been erected and removal of stucco beginning.

PHOTOGRAPH #23



**BUILDING 20
SECTION F**

Scaffolding has been erected and construction fencing placed at perimeter of work areas.
