

## PHOTOGRAPHS

PHOTOGRAPH #1



### BUILDING 1 SECTION H

Stucco sub-contractor installing stucco accessories. New GreenHeck louvers being installed at gable end.

PHOTOGRAPH #2



### BUILDING 1 SECTION H

Contractor preparing opening for installation of new GreenHeck louver.

**PHOTOGRAPH #3**



**BUILDING 1  
SECTION H**

Contractor preparing opening for installation of new GreenHeck louver.

**PHOTOGRAPH #4**



**BUILDING 1  
SECTION F**

Stucco sub-contractor has installed second water resistant barrier and begun installing stucco accessories.

**PHOTOGRAPH #5**



**BUILDING 1  
SECTION F**

Contractor has completed kick out flashings and flashed to sheathing with DuPont straight flash at balcony decks.

**PHOTOGRAPH #6**



**BUILDING 1  
SECTION D**

New 15/32" plywood sheathing installation in progress.

**PHOTOGRAPH #7**



**BUILDING 1  
SECTION C**

Simson Strong-Tie connectors and screws installed at top plates and roof trusses.

**PHOTOGRAPH #8**



**BUILDING 1  
SECTION C**

New 15/32" plywood sheathing installation in progress.

**PHOTOGRAPH #9**



**BUILDING 1  
SECTION C**

Required spacing has not been provided between plywood sheathing at a few locations. Contractor has been notified for corrections.

**PHOTOGRAPH #10**



**BUILDING 1  
SECTION B**

Installation of Simpson Strong-Tie strap connectors in progress.

**PHOTOGRAPH #11**



**BUILDING 1  
SECTION B**

Full framing repairs in progress at damaged balconies.

**PHOTOGRAPH #12**



**BUILDING 1  
SECTION A**

Framing repairs performed at damaged window headers and openings. Interior drywall has been removed by homeowners.

**PHOTOGRAPH #13**



**BUILDING 2  
SECTION H**

Removal of stucco and preexisting ThermoPly performed. Damaged framing observed and marked for repairs.

**PHOTOGRAPH #14**



**BUILDING 2  
SECTION H**

Removal of stucco and preexisting ThermoPly performed. Damaged framing observed and marked for repairs.

**PHOTOGRAPH #15**



**BUILDING 2  
SECTION H**

Damaged framing marked for repairs at second floor bottom plate and first floor window header.


**PHOTOGRAPH #16**



**BUILDING 2  
SECTION H**

Damaged framing marked for repairs at second floor bottom plate and window opening framing.

**PHOTOGRAPH #17**

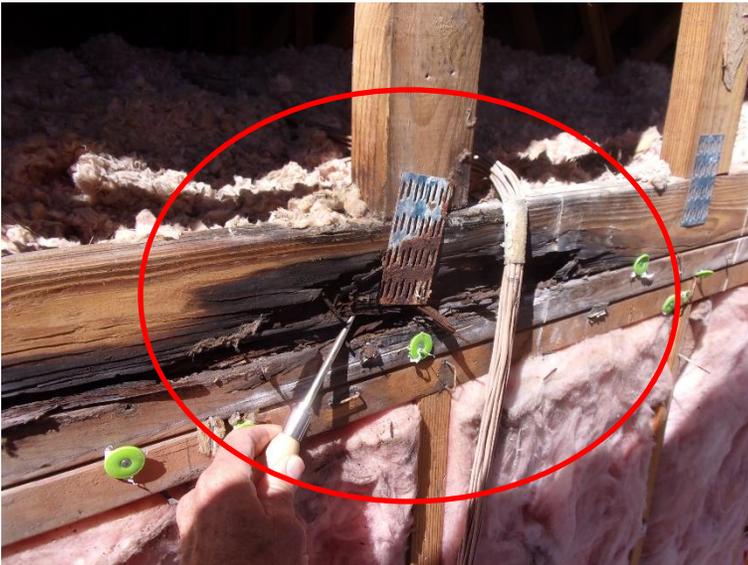

**BUILDING 2  
SECTION H**

Wood rot damage marked for repairs at  
gable end roofing truss.
