

## PHOTOGRAPHS

PHOTOGRAPH #1



### BUILDING 1 SECTION H

New GreenHeck louvers installed and prepared for stucco application at gable end.

PHOTOGRAPH #2



### BUILDING 1 SECTION H

Stucco contractor has completed lath and stucco accessories.


**PHOTOGRAPH #3**



**BUILDING 1  
SECTION G**

Stucco contractor has completed lath and stucco accessories.

**PHOTOGRAPH #4**

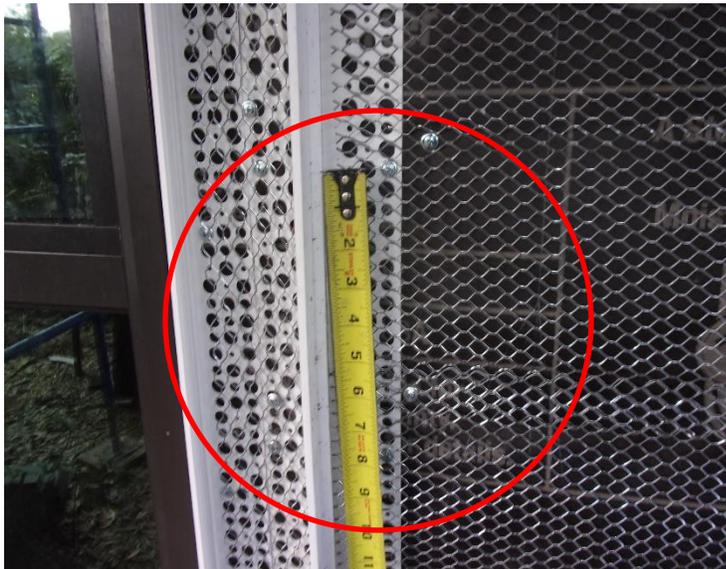

**BUILDING 1  
SECTION G**

Lathing and stucco accessories fastening in compliance with specifications.

**PHOTOGRAPH #5**



**BUILDING 1  
SECTION F**

Stucco contractor in process of applying Vinyl Corp. stucco accessories, joints, and casing beads.

**PHOTOGRAPH #6**



**BUILDING 1  
SECTION E**

Stucco contractor in process of applying Vinyl Corp. stucco accessories, joints, and casing beads.

**PHOTOGRAPH #7**



**BUILDING 1  
SECTION D**

Plywood sheathing installed and Tyvek WRB wrap in progress.

**PHOTOGRAPH #8**



**BUILDING 1  
SECTION D**

New PGT window installed with Dupont / Tyvek flashing system.


**PHOTOGRAPH #9**



**BUILDING 1  
SECTION D**

Interior gaps between window frame and jamb in compliance with manufacturers NOAs.


**PHOTOGRAPH #10**

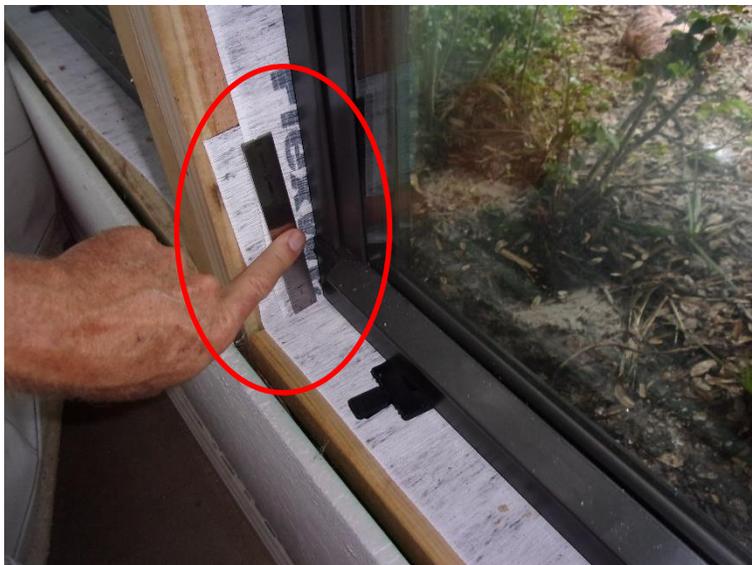

**BUILDING 1  
SECTION D**

Overlapping of Dupont flashings at window opening in compliance with manufactures instructions and specifications.


**PHOTOGRAPH #11**

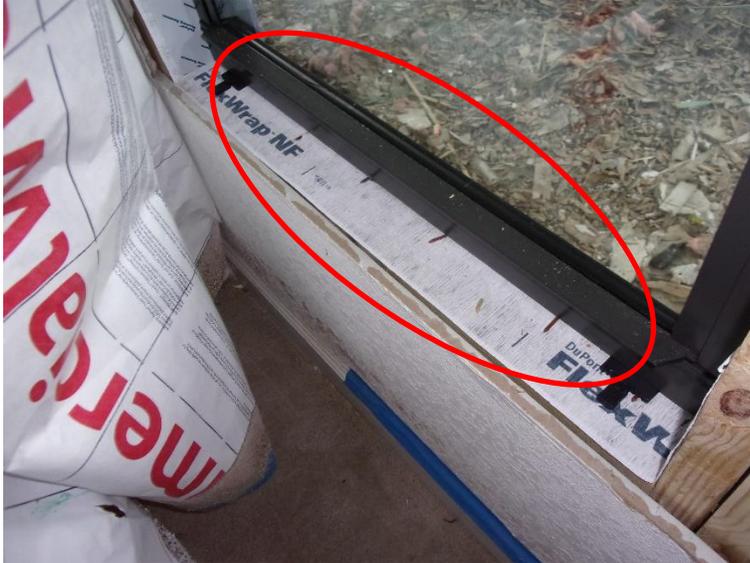

**BUILDING 1  
SECTION D**

Nails installed at improper angle have penetrated flashing at windowsill.

**PHOTOGRAPH #12**

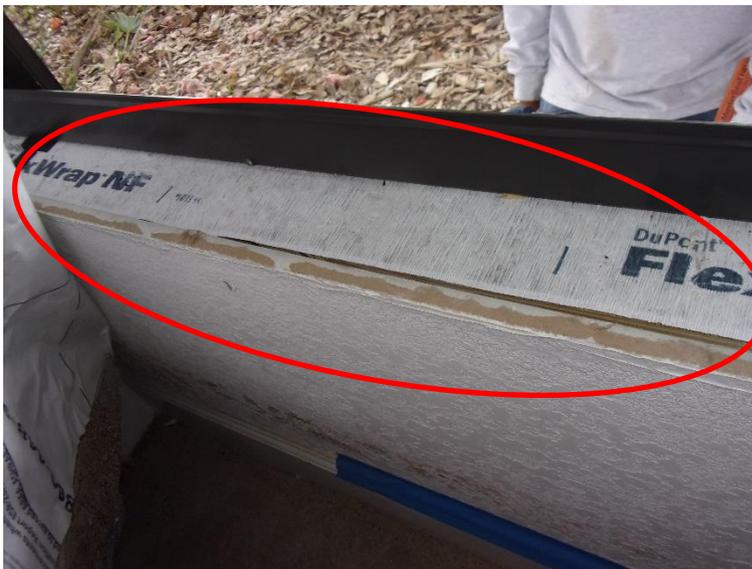

**BUILDING 1  
SECTION D**

Corrections performed were nails penetrated flashing at windowsill.

**PHOTOGRAPH #13**



**BUILDING 2  
SECTION D**

Nails installed at improper angle have penetrated flashing at windowsill.

**PHOTOGRAPH #14**



**BUILDING 2  
SECTION D**

Corrections performed were nails penetrated flashing at windowsill.

**PHOTOGRAPH #15**



**BUILDING 2  
SECTION D**

New PGT window fastened at flange as per specifications.

**PHOTOGRAPH #16**



**BUILDING 2  
SECTION C**

Window installation in progress. Contractor utilizing primer for proper adhesion of Dupont flashings.

**PHOTOGRAPH #17**



**BUILDING 2  
SECTION B**

Simpson Strong-Tie straps installed improperly at top and several subfloor locations.

**PHOTOGRAPH #18**



**BUILDING 2  
SECTION B**

Contractor has corrected strapping where improperly applied at several locations.

**PHOTOGRAPH #19**



**BUILDING 2  
SECTION B**

Florida Paint Ultra Supercoat acrylic being applied at patio ceilings and walls.

**PHOTOGRAPH #20**



**BUILDING 2  
SECTION B**

Florida Paint Ultra Supercoat acrylic being applied at patio ceilings and walls.

**PHOTOGRAPH #21**



**BUILDING 2  
SECTION B**

Required spacing not been provided between plywood sheathing at a few locations.

**PHOTOGRAPH #22**



**BUILDING 2  
SECTION B**

Contractor has corrected spacing at plywood sheathing where observed.

**PHOTOGRAPH #23**



**BUILDING 2  
SECTION A**

Simpson Strong -Tie connectors and anchors installed as per drawings and specifications.

**PHOTOGRAPH #24**



**BUILDING 2  
SECTION A**

Simpson Strong -Tie connectors and anchors installed as per drawings and specifications.
