

PHOTOGRAPHS

PHOTOGRAPH #1



**BUILDING 1
SECTION G**

Florida Paints primer and finish paint applied.

PHOTOGRAPH #2



**BUILDING 1
SECTION G- UNIT # 122**

Drywall repairs in progress at interior window openings.

PHOTOGRAPH #3



**BUILDING 1
SECTION F**

Roof kick out details incomplete. Full bed of roofing mastic required prior to reinstallation of tiles and final details.


PHOTOGRAPH #4



**BUILDING 1
SECTION E**

Stucco finishes applied and Florida Paints primer coat in progress.

PHOTOGRAPH #5

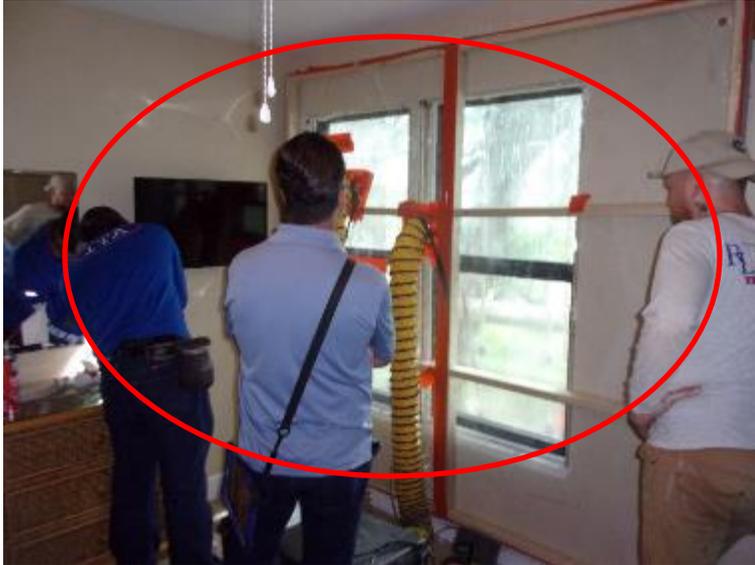

**BUILDING 1
SECTION E – UNIT #128**

Independent Testing agency performing AAMA 502 testing at double windows.

PHOTOGRAPH #6



**BUILDING 1
SECTION E – UNIT #128**

Testing failed allowing water penetration at left bottom corner of right window.

PHOTOGRAPH #7



**BUILDING 1
SECTION E – UNIT #128**

Testing failed allowing water penetration at left bottom corner of right window.

PHOTOGRAPH #8



**BUILDING 1
SECTION D – UNIT #128**

Independent Testing agency performing AAMA 502 testing at double windows.

PHOTOGRAPH #9



**BUILDING 1
SECTION D – UNIT #128**

Testing failed allowing water penetration at bottom of right window. Retesting successful after sealant remediation performed with silicone sealant at window framing.

PHOTOGRAPH #10



**BUILDING 1
SECTION D / UNIT #118**

Drywall, windowsill repairs and texture performed at window openings.

PHOTOGRAPH #11



**BUILDING 1
SECTION D**

Stucco contractor performing scratch and brown coats of stucco.


PHOTOGRAPH #12



**BUILDING 1
SECTION C**

Stucco contractor applying stucco accessories and lathing.

PHOTOGRAPH #13

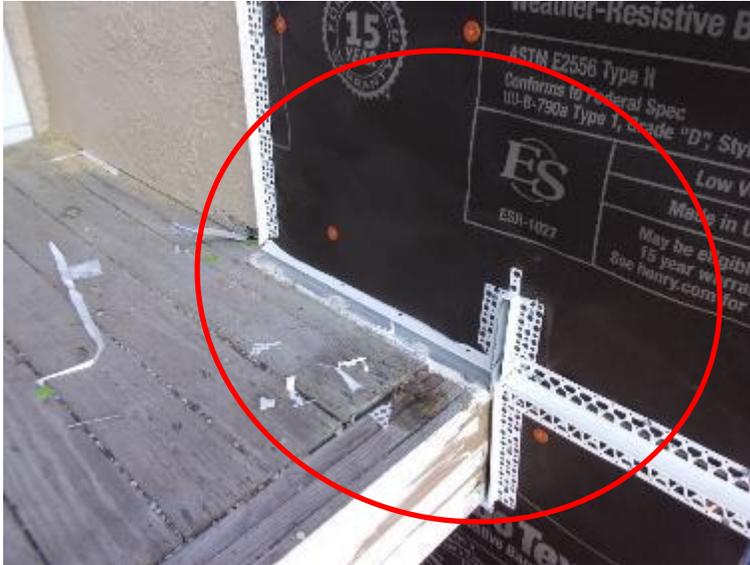

**BUILDING 1
SECTION B**

Kick out flashing details installed with stucco accessories at balcony edges.

PHOTOGRAPH #14



**BUILDING 1
SECTION A**

Super Jumbo Tex 60 WRB applied over Tyvek WRB.

PHOTOGRAPH #15



**BUILDING 2
SECTION H**

Framing repairs, strapping, connectors, Termite protection and wood preservative performed.

PHOTOGRAPH #16



**BUILDING 2
SECTION H**

Borra Care Termite treatment applied by pest sub-contractor.

PHOTOGRAPH #17



**BUILDING 2
SECTION H**

Simpson Strong-Tie connectors and anchors installed according to drawings and specifications.

PHOTOGRAPH #18



**BUILDING 2
SECTION H**

Simpson Strong-Tie straps installed according to drawings and specifications.

PHOTOGRAPH #19



**BUILDING 2
UNIT #221 - ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #20



**BUILDING 2
UNIT #221 - ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #21



**BUILDING 2
UNIT #222 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #22



**BUILDING 2
UNIT #222 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #23



**BUILDING 2
SECTION G**

Breezeway beam collapsed when stucco was removed.

PHOTOGRAPH #24



**BUILDING 2
SECTION G-BREEZEWAY**

Entry doors sanded in preparation for prim coat of paint.

PHOTOGRAPH #25



**BUILDING 2
SECTION F**

Contractor has erected access scaffold and begun removal of stucco.

PHOTOGRAPH #26



**BUILDING 2
UNIT #224 – ATTIC**

Holes in new fire caulk require contractor to repair.

PHOTOGRAPH #27



**BUILDING 2
UNIT #224 – ATTIC**

Contractor has repaired holes in new fire caulk.

PHOTOGRAPH #28



**BUILDING 2
UNIT #224 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #29



**BUILDING 2
UNIT #226 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #30



**BUILDING 2
UNIT #226 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #31



**BUILDING 2
UNIT #228 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #32



**BUILDING 2
UNIT #228 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #33



**BUILDING 2
UNIT #227 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #34



**BUILDING 2
UNIT #227– ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #35



**BUILDING 2
UNIT #225 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #36



**BUILDING 2
UNIT #225 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #37



**BUILDING 2
UNIT #223 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.

PHOTOGRAPH #38



**BUILDING 2
UNIT #223 – ATTIC**

Gusset, scabs, and fire wall repairs performed and quantified.
