

PHOTOGRAPHS

PHOTOGRAPH #1



**BUILDING 2
SECTION H**

Contractor has attached and painted electrical wiring cover and re attached A/C electrical boxes.

PHOTOGRAPH #2



**BUILDING 2
SECTION G**

Contractor has replaced rotted cedar door framing at patio.


PHOTOGRAPH #3



**BUILDING 2
SECTION G**

Stair way railings and steps finish painted with Florida Paints coatings.

PHOTOGRAPH #4

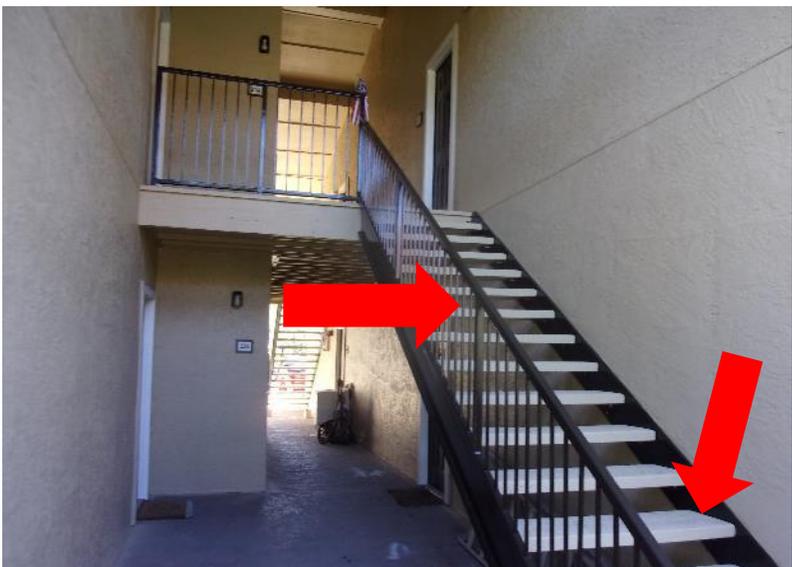

**BUILDING 2
SECTION E**

Stair way railings and steps finish painted with Florida Paints coatings.

PHOTOGRAPH #5



**BUILDING 2
SECTION D**

A/C electrical boxes have not been re attached or sealed to the new stucco.

PHOTOGRAPH #6



**BUILDING 2
SECTION D**

Six-inch distance from stucco to grade per drawings has not been meet and is the responsibility of owners to be performed by others.

PHOTOGRAPH #7



**BUILDING 2
SECTION B**

Balcony railings have been reinstalled by anchoring to the built-up beam at railing stanchions.

PHOTOGRAPH #8



**BUILDING 2
SECTION A**

Bottom two steps require removal, angle reinforcement welding at stringers and re installation. Contractor performing as change order repairs.

PHOTOGRAPH #9



**BUILDING 2
SECTION A**

New precast concrete steps delivered for change order repairs at stairways.

PHOTOGRAPH #10



**BUILDING 3
SECTION H**

Contractor has applied Tyvek HomeWrap over new plywood sheathing, covering window openings until windows are delivered.

PHOTOGRAPH #11



**BUILDING 3
SECTION H**

Locations marked for corrections where seam tape improperly used at penetrations.

PHOTOGRAPH #12



**BUILDING 3
SECTION G**

Contractor has applied Tyvek HomeWrap over new plywood sheathing, covering window openings until windows are delivered.

PHOTOGRAPH #13



**BUILDING 3
SECTION F**

Corrections made at gaps greater than 1/4" with sealant and partially driven nails re set.

PHOTOGRAPH #14



**BUILDING 3
SECTION F**

Contractor has applied Tyvek HomeWrap over new plywood sheathing, covering window openings until windows are delivered.

PHOTOGRAPH #15



**BUILDING 3
SECTION E**

Corrections made at gaps greater than 1/4" with sealant and nails replaced where marked.

PHOTOGRAPH #16



**BUILDING 3
SECTION E**

Contractor has applied Tyvek HomeWrap over new plywood sheathing, covering window openings until windows are delivered.

PHOTOGRAPH #17



**BUILDING 6
SECTION H**

Access scaffolding erected and stucco cutting for removal has begun.

PHOTOGRAPH #18



**BUILDING 6
SECTION G**

Access scaffolding erected, balcony railing removed and stucco cutting for removal has begun.

PHOTOGRAPH #19



**BUILDING 6
SECTION F**

Contractor has set up access scaffolding and construction fencing.
