

PHOTOGRAPHS


PHOTOGRAPH #1



**BUILDING 7
SECTION A**

Contractor has applied JumboTex water resistant barrier over Tyvek HomeWrap.

PHOTOGRAPH #2

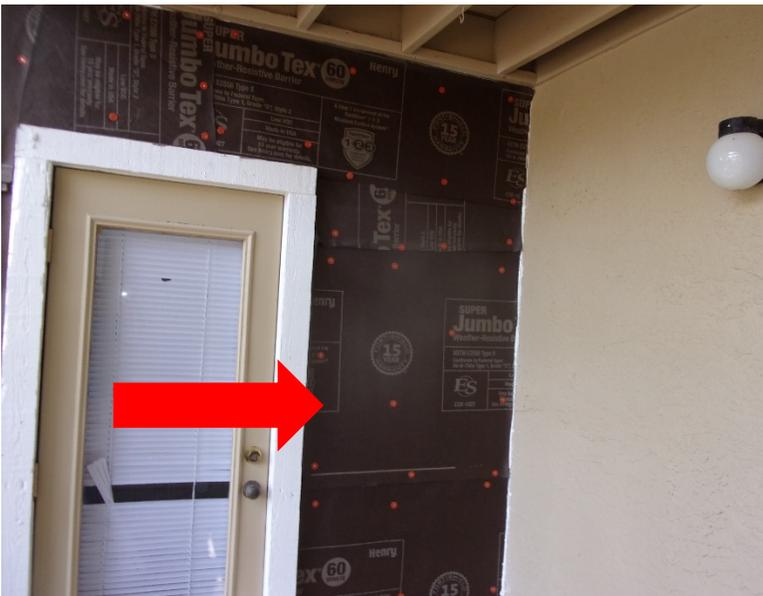

**BUILDING 7
SECTION A**

Additional stucco removed, re sheathed and covered with JumboTex past Lani door to corner of Lani as required from action items.

PHOTOGRAPH #3



**BUILDING 7
SECTION A**

Additional stucco removed, re sheathed and covered with JumboTex at header over Lanai door as required from action items.

PHOTOGRAPH #4



**BUILDING 7
SECTION A**

Simson Strong-Tie #SDW22458 screws and shear clip installed at built up beam as per drawings.

PHOTOGRAPH #5



**BUILDING 7
SECTION B**

JumboTex 60 Water resistant barrier applied over Tyvek HomeWrap.

PHOTOGRAPH #6



**BUILDING 7
SECTION B**

Contractor installing vinyl stucco accessories at new windows.

PHOTOGRAPH #7



**BUILDING 7
SECTION C**

Unit #717 - Independent Testing agency performed AAMA 502 water testing at single window with no leaks or failures.

PHOTOGRAPH #8



**BUILDING 7
SECTION C**

Unit #717 - Independent Testing agency performed AAMA 502 water testing at single window with no leaks or failures

PHOTOGRAPH #9



**BUILDING 7
SECTION D**

Unit #717 - Independent Testing agency performed AAMA 502 water testing at double windows with leak failure at lower left corner sill.

PHOTOGRAPH #10



**BUILDING 7
SECTION D**

Unit #717 - Independent Testing agency performed AAMA 502 water testing at Double windows with leak failure at lower left corner sill.

PHOTOGRAPH #11



**BUILDING 7
SECTION D**

Unit #717 - Independent Testing agency performed AAMA 502 water testing at Double windows with leak failure at lower left corner sill.

PHOTOGRAPH #12



**BUILDING 7
SECTION D**

Contractor has installed prepared and primed new wood soffit and vinyl venting at soffit as per drawings.

PHOTOGRAPH #13



**BUILDING 7
SECTION E**

Stucco sub-contractor has applied scratch coat of stucco over self-furring galvanized metal lath.

PHOTOGRAPH #14



**BUILDING 7
SECTION F**

Stucco subcontractor in process of applying 7/8" three coat stucco system.

PHOTOGRAPH #15



**BUILDING 7
SECTION F**

Stucco sub-contractor has applied scratch coat of stucco over self-furring galvanized metal lath.

PHOTOGRAPH #16



**BUILDING 7
SECTION G**

Metal lathing exposed thru scratch coat and holes in scratch coat exposing metal lathing.


PHOTOGRAPH #17



**BUILDING 7
SECTION H**

Stucco sub-contractor applying scratch coat of stucco over self-furring galvanized metal lath.

PHOTOGRAPH #18

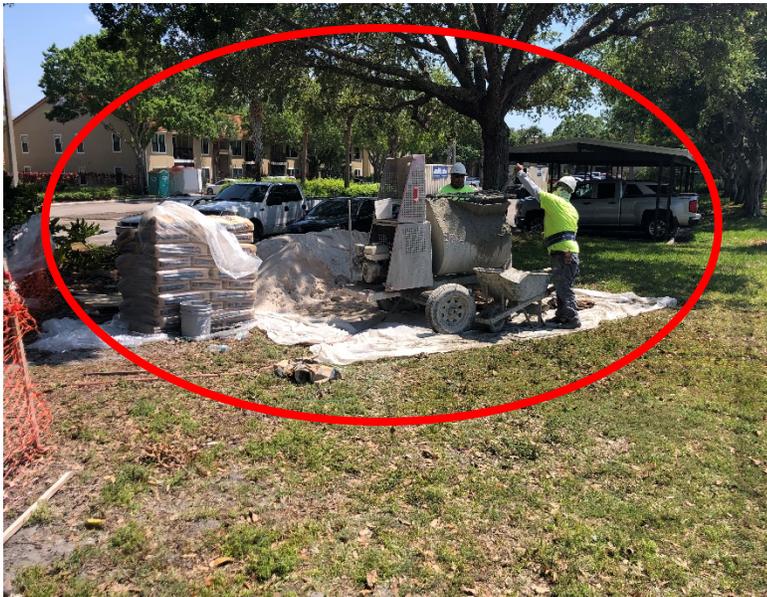

**BUILDING 7
SECTION H**

Stucco contractor mixing Broco bagged stucco cement with sand on site.

PHOTOGRAPH #19



**BUILDING 8
SECTION H**

Contractor has begun installing 15/32" plywood sheathing at gable end wall.

PHOTOGRAPH #20



**BUILDING 8
SECTION H**

New GreenHeck Louvers being installed at gable end attic space.

PHOTOGRAPH #21



**BUILDING 8
SECTION H**

Copper Green wood preservative has been applied at bottom plate and framing studs.

PHOTOGRAPH #22



**BUILDING 8
SECTION H**

Copper Green wood preservative has been applied at bottom plate and framing studs.

PHOTOGRAPH #23



**BUILDING 8
SECTION H**

Bora Care termite treatment has been applied to gable end wall framing as per specifications.

PHOTOGRAPH #24



**BUILDING 8
SECTION G**

Copper Green wood preservative has been applied at bottom plate and framing studs.

PHOTOGRAPH #25



**BUILDING 8
SECTION G**

Contractor has instilled Simpson Strong - Tie connection hardware at header to top plate, top plate to trusses and wall studs to top plate as per drawings.

PHOTOGRAPH #26



**BUILDING 8
SECTION G**

Unit # 822- Balcony decking damaged by carpet covering will require replacement.

PHOTOGRAPH #27



**BUILDING 8
SECTION G**

New Breezeway box beam installed and Simpson Strong -Tie connectors in place per drawings.
