

PHOTOGRAPHS


PHOTOGRAPH #1



**BUILDING 7
SECTION A**

Unit #711- Contractor has removed and replaced double window header from interior side.

PHOTOGRAPH #2

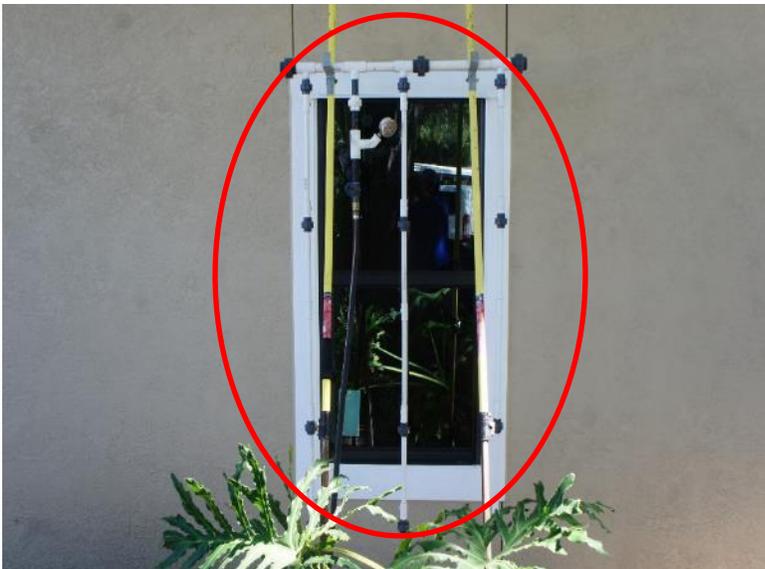

**BUILDING 7
SECTION A**

Unit #711- Added Single window tested by Independent Testing Agency as per ASTM 502 passed with no leaks.


PHOTOGRAPH #3



**BUILDING 7
SECTION A**

Unit #711- Added Single window tested by Independent Testing Agency as per ASTM 502 passed with no leaks.

PHOTOGRAPH #4

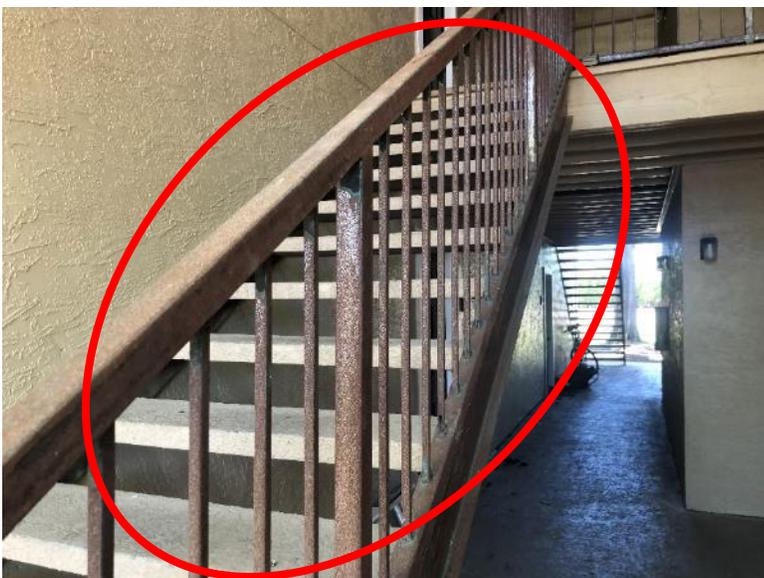

**BUILDING 7
SECTION A**

Previously prepared steel railings have begun to show surface rust and will require light sanding and solvent wipe as per manufacturer's guidelines before priming.

PHOTOGRAPH #5



**BUILDING 7
SECTION C**

Previously prepared steel railings have begun to show surface rust and will require light sanding and solvent wipe as per manufacturer's guidelines before priming.

PHOTOGRAPH #6



**BUILDING 7
SECTION D**

Unit #717- Double window retested by Independent Testing Agency as per ASTM 502 passed with no leaks.

PHOTOGRAPH #7



**BUILDING 7
SECTION D**

Unit #717- Double window retested by Independent Testing Agency as per ASTM 502 passed with no leaks

PHOTOGRAPH #8



**BUILDING 7
SECTION D**

Delta performed weather seal joint standard field adhesion test at bottom left ground floor double windows by marking and cutting sealant from substrates and hand pulling sealant to cohesive failure. Test passed with proper adhesion.

PHOTOGRAPH #9



**BUILDING 7
SECTION D**

Delta performed weather seal joint standard field adhesion test at bottom left ground floor double windows by marking and cutting sealant from substrates and hand pulling sealant to cohesive failure. Test passed with proper adhesion.

PHOTOGRAPH #10



**BUILDING 7
SECTION D**

Delta performed weather seal joint standard field adhesion test at bottom left ground floor double windows by marking and cutting sealant from substrates and hand pulling sealant to cohesive failure. Test passed with proper adhesion

PHOTOGRAPH #11



**BUILDING 7
SECTION D**

Unit #718- Contractor in process of interior sealants and drywall repairs.

PHOTOGRAPH #12



**BUILDING 7
SECTION D**

Unit #718- New sealant applied at window perimeter from Dupont flashing to new PGT window.

PHOTOGRAPH #13



**BUILDING 7
SECTION G**

Unit #712- Contractor in process of interior sealants and drywall repairs

PHOTOGRAPH #14



**BUILDING 7
SECTION G**

Unit #712- New sealant applied at window perimeter from Dupont flashing to new PGT window.


PHOTOGRAPH #15



**BUILDING 8
SECTION H**

Sub-Contractor has Installed self-furring galvanized metal lathing and Vinyl stucco accessories at Gable end wall.

PHOTOGRAPH #16

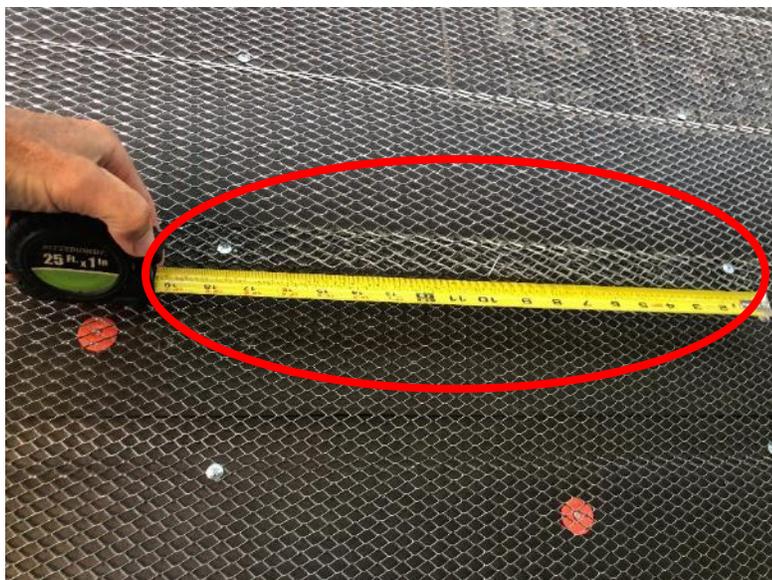

**BUILDING 8
SECTION H**

Self-furring galvanized metal lathing attached at wall framing 16" O.C. and wired together at overlaps between framing members.

PHOTOGRAPH #17



**BUILDING 8
SECTION G**

Urethane sealant applied at new vinyl accessory intersections, transitions, and butt joints.

PHOTOGRAPH #18



**BUILDING 8
SECTION G**

Contactor has installed and painted new soffit and vinyl venting.

PHOTOGRAPH #19



**BUILDING 8
SECTION F**

Sub-Contractor installing self-furring galvanized metal lathing and Vinyl stucco accessories at exterior bearing walls.

PHOTOGRAPH #20



**BUILDING 8
SECTION F**

Sub-Contractor installing self-furring galvanized metal lathing and Vinyl stucco accessories at exterior bearing walls.

PHOTOGRAPH #21



**BUILDING 8
SECTION F**

New kick out flashing details installed at balcony decks as per PM drawings.

PHOTOGRAPH #22



**BUILDING 8
SECTION E**

Super Jumbo Tex 60 applied as second water resistant barrier.

PHOTOGRAPH #23



**BUILDING 8
SECTION E**

Super Jumbo Tex 60 applied as second water resistant barrier.

PHOTOGRAPH #24



**BUILDING 8
SECTION A**

Contractor has prepared and primed entrance doors with Florida Paints anti corrosive primer.

PHOTOGRAPH #25



**BUILDING 8
SECTION A**

Contractor spray painting entrance doors with All Grip exterior finish paint.

PHOTOGRAPH #26



**BUILDING 8
SECTION A**

Contractor spray painting entrance doors with All Grip exterior finish paint.

PHOTOGRAPH #27



**BUILDING 13
SECTION H**

Contractor has erected access scaffolding and begun cutting existing stucco for removal.

PHOTOGRAPH #28



**BUILDING 13
SECTION F**

Contractor has erected access scaffolding for repairs.

PHOTOGRAPH #29



**BUILDING 13
SECTION F**

Contractor has provided construction fencing designating hard hat construction areas.

PHOTOGRAPH #30



**BUILDING 13
SECTION E**

Contractor has erected access scaffolding for repairs.
