

PHOTOGRAPHS


PHOTOGRAPH #1



**BUILDING 7
SECTION A**

Unit #721- Contractor has performed interior drywall, sill repairs and priming of new repairs surfaces.

PHOTOGRAPH #2

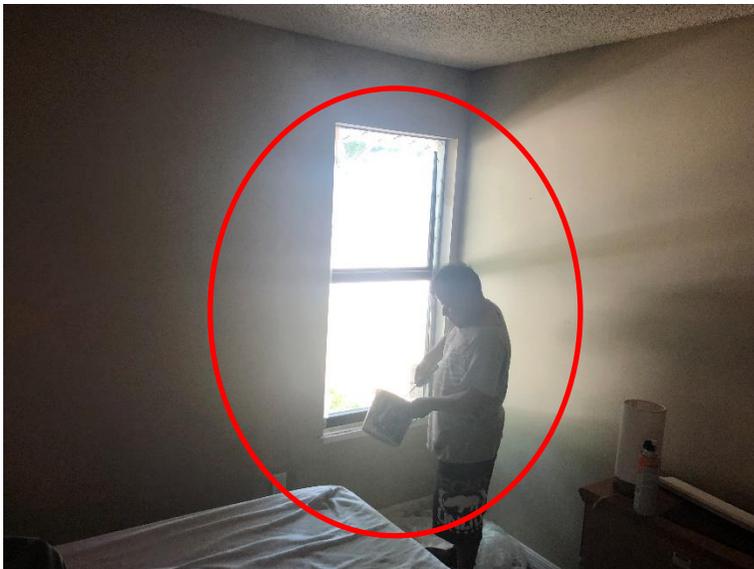

**BUILDING 7
SECTION A**

Unit #721- Contractor has performed interior drywall, sill repairs and priming of new repairs surfaces.

PHOTOGRAPH #3



**BUILDING 7
SECTION A- BREEZEWAY**

Contractor has left repair materials and debris in walk areas.

PHOTOGRAPH #4



**BUILDING 7
SECTION C- BREEZEWAY**

Contractor has left repair materials and debris in walk areas.

PHOTOGRAPH #5



**BUILDING 7
SECTION C**

Contractor has left repair materials and debris scattered around exterior grounds.

PHOTOGRAPH #6



**BUILDING 8
SECTION H**

Sub-Contractor has completed installing self-furring galvanized metal lathing and Vinyl stucco accessories around electrical boxes.

PHOTOGRAPH #7



**BUILDING 8
SECTION G**

Sub-Contractor has completed Installing self-furring galvanized metal lathing and Vinyl stucco accessories in preparation for stucco application.

PHOTOGRAPH #8



**BUILDING 8
SECTION G**

Unit #822- New pressure treated 2"x6" decking installed to replace existing damaged decking.


PHOTOGRAPH #9



**BUILDING 8
SECTION F**

New kick out flashing details and vinyl stucco accessories installed at balcony decks as per PM drawings.

PHOTOGRAPH #10

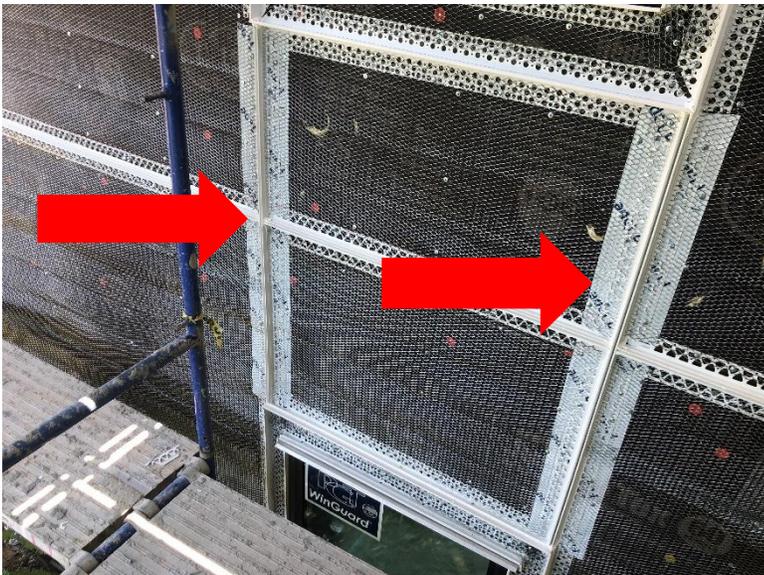

**BUILDING 8
SECTION E**

Sub-Contractor installing self-furring galvanized metal lathing and Vinyl stucco accessories at exterior bearing walls has applied Dupont flashing behind vertical control joints as per drawings.

PHOTOGRAPH #11



**BUILDING 8
SECTION D**

Contractor has begun gable end reinforcement and wall bracing repairs.

PHOTOGRAPH #12



**BUILDING 8
SECTION D**

Contractor has retrofit gable end studs with 2"X4" SYP and in process of installing cross braces in attic space as per drawings and specifications.

PHOTOGRAPH #13



**BUILDING 8
SECTION D**

Plastic tarps used for protection of open walls during construction, does not cover open gable end attic space.

PHOTOGRAPH #14



**BUILDING 8
SECTION C**

Unit #828- Upper balcony repairs in progress at built up beam and support framing.

PHOTOGRAPH #15



**BUILDING 8
SECTION B**

Contractor has protected open walls with heavy plastic tarps during repairs.

PHOTOGRAPH #16



**BUILDING 8
SECTION A**

Pressure treated 2"X10" SYP delivered to site for building new built-up beams at balconies.

PHOTOGRAPH #17



**BUILDING 13
SECTION H**

Contractor has removed existing stucco at gable end wall leaving section behind electrical meters as per drawings.

PHOTOGRAPH #18



**BUILDING 13
SECTION H**

Window header damaged by wood rot and termites exposed upon stucco removal.

PHOTOGRAPH #19



**BUILDING 13
SECTION H**

Contractor has protected open walls with heavy plastic tarps during repairs.

PHOTOGRAPH #20



**BUILDING 13
SECTION G**

Contractor has protected open walls with heavy plastic tarps during repairs.

PHOTOGRAPH #21



**BUILDING 13
SECTION F**

Contractor in process of removing stucco and excising sheathing.

PHOTOGRAPH #22



**BUILDING 13
SECTION E**

Breezeway box beam damaged by wood rot and termites exposed upon stucco removal.
