


**PHOTOGRAPH #1**



**BUILDING 11  
SECTION H**

Contractor has performed gable end wall bracing repairs and set in place new gable end louvers.

**PHOTOGRAPH #2**

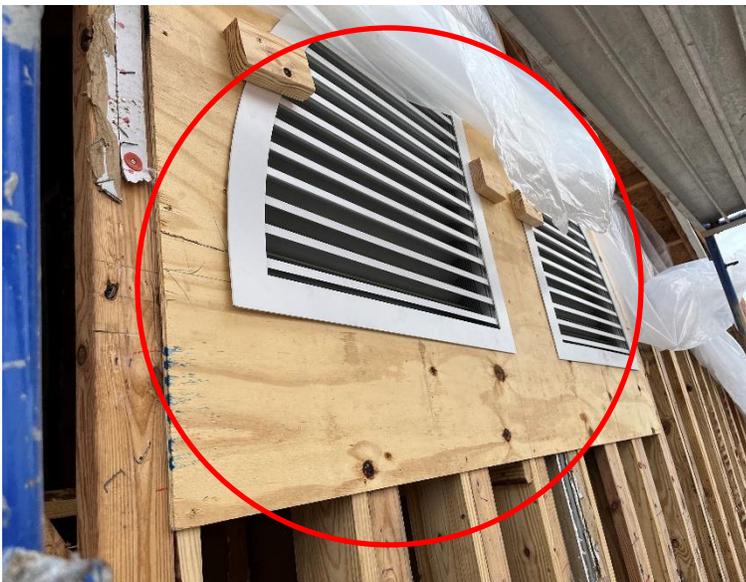

**BUILDING 11  
SECTION H**

Green Heck louvers preset into new framing and structural plywood sheathing.

**PHOTOGRAPH #3**



**BUILDING 11  
SECTION H**

Cross bracing @ 48" O.C. fastened to top chord and bottom chord as per drawings.

**PHOTOGRAPH #4**



**BUILDING 11  
SECTION H**

New retrofit 2x6 studs nailed to existing vertical 2x4 framing at gable end as per drawings.

**PHOTOGRAPH #5**



**BUILDING 11  
SECTION H**

Simpson Strong-Tie # LSTA-21 strap fastened at lateral bracing to retrofit studs at gable end framing.

**PHOTOGRAPH #6**



**BUILDING 11  
SECTION F**

Damaged triple header above windows replaced with new header and strapped over with Simpson Strong-Tie MSTA 49 straps.

**PHOTOGRAPH #7**



**BUILDING 11  
SECTION F**

Bottom plate sealed to existing concrete footing with BASF MasterSeal NP 150 .

**PHOTOGRAPH #8**



**BUILDING 11  
SECTION F**

Bottom plate sealed to existing concrete footing with BASF MasterSeal NP 150.

**PHOTOGRAPH #9**



**BUILDING 11  
UNIT #1115**

Contractor has applied new BASF sealant at door frame to stucco transitions.

**PHOTOGRAPH #10**



**BUILDING 12  
SECTION H**

Contractor has begun gable end wall bracing repairs and covered open wall with protective plastic.

**PHOTOGRAPH #11**



**BUILDING 12  
SECTION H**

Contractor installing new framing for louver vents and providing new retrofit 2x6 studs nailed to existing vertical 2x4 framing at gable end as per drawings.

**PHOTOGRAPH #12**



**BUILDING 12  
SECTION H**

New Green Heck E HH 601 louvers ready for installation.

**PHOTOGRAPH #13**



**BUILDING 12  
SECTION G**

Contractor erected access scaffolding, safety fencing and begun cutting stucco for removal.

**PHOTOGRAPH #14**



**BUILDING 12  
SECTION F**

Contractor erected access scaffolding, safety fencing and begun cutting stucco for removal.

**PHOTOGRAPH #15**



**BUILDING 12  
SECTION E**

Contractor erected access scaffolding, safety fencing and begun cutting stucco for removal.

**PHOTOGRAPH #16**



**BUILDING 12  
SECTION D**

Landscaping is above bottom of wall requiring repairs.
