

PHOTOGRAPH #1



**BUILDING 12
ATTIC REPAIRS -UNIT #1221**

Contractor has performed scab repairs at damaged trusses as per drawings.

PHOTOGRAPH #2



**BUILDING 12
ATTIC REPAIRS -UNIT #1221**

Contractor has multiple fire wall repairs as per specifications.

PHOTOGRAPH #3



**BUILDING 12
ATTIC REPAIRS - UNIT #1223**

Contractor has performed gusset repairs at damaged truss connectors as per drawings.

PHOTOGRAPH #4



**BUILDING 12
ATTIC REPAIRS - UNIT #1223**

Contractor has performed fire board and fire caulk repairs at penetrations of fire wall.

PHOTOGRAPH #5



**BUILDING 12
ATTIC REPAIRS - UNIT #1223**

Contractor has performed scab repairs at damaged trusses as per drawings.

PHOTOGRAPH #6



**BUILDING 12
ATTIC REPAIRS - UNIT #1223**

Contractor has performed scab repairs at damaged trusses as per drawings.

PHOTOGRAPH #7



**BUILDING 12
ATTIC REPAIRS - UNIT #1222**

Contractor has performed fire wall repairs as per specifications.

PHOTOGRAPH #8



**BUILDING 12
SECTION G-BREEZEWAYS**

Contractor has sealed cracks in cedar beams.

PHOTOGRAPH #9



**BUILDING 9
SECTION H**

Contractor has begun painting new stucco with Florida Paints Acrylic Paint.


PHOTOGRAPH #10



**BUILDING 9
SECTION F**

Stucco sub-contract applying scratch coat of new stucco.

PHOTOGRAPH #11

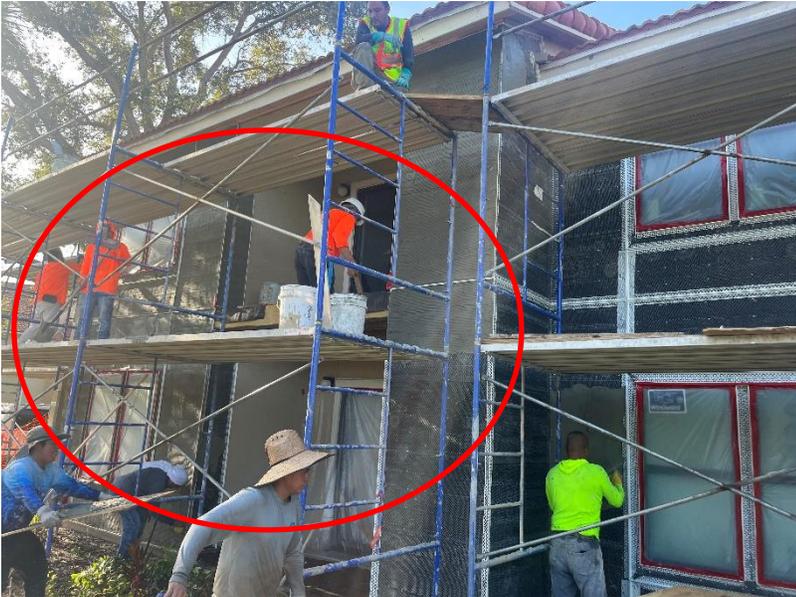

**BUILDING 9
SECTION E**

Stucco sub-contract applying scratch coat of new stucco.

PHOTOGRAPH #12



**BUILDING 9
SECTION E**

Stucco sub-contractor mixing sand with CEMEX Broco stucco cement bag mix.

PHOTOGRAPH #13



**BUILDING 9
SECTION D**

Unit #918- New window framed and installed in wrong location not lining up with other windows.

PHOTOGRAPH #14



**BUILDING 9
SECTION D**

Unit #918- Contractor removed, reframed, and reinstalled new PGT window in correct location.

PHOTOGRAPH #15



**BUILDING 9
SECTION D**

Contractor has installed new plywood soffit with vinyl vent as per specifications.


PHOTOGRAPH #16



**BUILDING 9
SECTION C**

Contractor has installed new plywood soffit with vinyl vent as per specifications.

PHOTOGRAPH #17

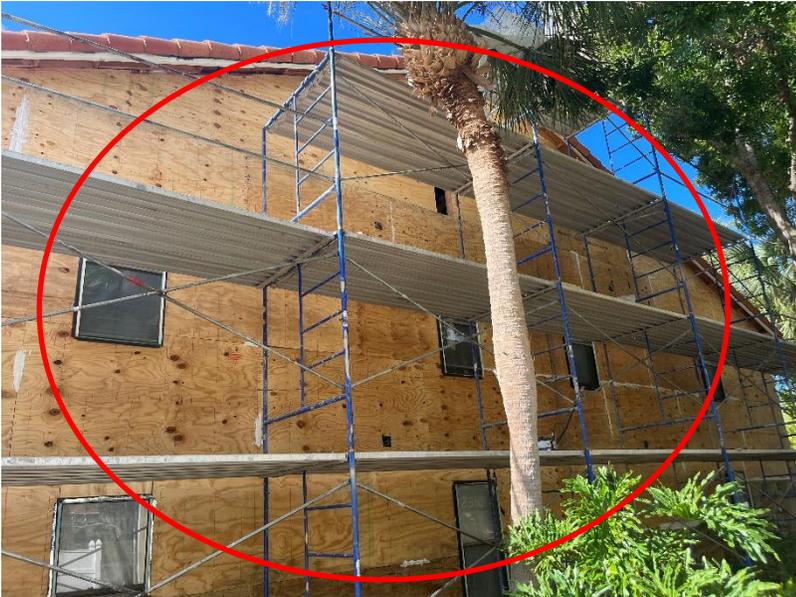

**BUILDING 15
SECTION H**

New 15/32" plywood sheathing installed at gable end wall.

PHOTOGRAPH #18



**BUILDING 15
SECTION H**

Bottom 4x8 sheets of sheathing installed with pressure treated plywood as per specifications.

PHOTOGRAPH #19



**BUILDING 15
SECTION H**

Bottom 4x8 sheets of sheathing installed with pressure treated plywood as per specifications.

PHOTOGRAPH #20



**BUILDING 15
SECTION G**

Termite contractor has applied Bora Care termite treatment to wall framing as per specification.

PHOTOGRAPH #21



**BUILDING 15
SECTION G**

Bottom plate fastened into existing footing with 5/8" Simpson Titen HD @ 24" O.C. as per drawings.

PHOTOGRAPH #22



**BUILDING 15
SECTION F**

Simpson MST A strap connectors installed from studs to studs at first to second floor transition as per drawings.

PHOTOGRAPH #23



**BUILDING 15
SECTION F**

Simpson Strong Tie connectors and screws attaching framing studs to top plate and top plate to roof trusses as per drawings.

PHOTOGRAPH #24



**BUILDING 15
SECTION E**

Contractor installing Simpson H3 connector at box beam to stud as per drawings.

PHOTOGRAPH #25



**BUILDING 15
SECTION E**

Wall framing studs attached to bottom plate with Simpson SP1 connectors as per drawings.
