

PHOTOGRAPHS

PHOTOGRAPH #1



**BUILDING 5
UNIT #526- PUNCH**

Living room middle operable window has been repaired by PGT service team.

PHOTOGRAPH #2



**BUILDING 5
UNIT #528- PUNCH**

Bedroom right operable window has been repaired by PGT service team.

PHOTOGRAPH #3



**BUILDING 23
UNIT #2325- PUNCH**

Broken window has been replaced by PGT service team.

PHOTOGRAPH #4



**BUILDING 23
SECTION F- PUNCH LIST**

Damaged screen at lower porch has been repaired.

PHOTOGRAPH #5



**BUILDING 21
SECTION F**

Stucco sub-contractors applying brown coat of stucco.

PHOTOGRAPH #6



**BUILDING 21
SECTION D**

Stucco sub-contractors applying scratch coat of stucco.

PHOTOGRAPH #7



**BUILDING 21
SECTION C**

Stucco subcontractor applying new stucco accessories and metal lathing.

PHOTOGRAPH #8



**BUILDING 21
SECTION B**

Stucco subcontractors have applied JumboTex Super 60 water resistant barrier and begun application of new stucco accessories.

PHOTOGRAPH #9



**BUILDING 21
SECTION B**

New galvanized kick out flashing installed at balconies.

PHOTOGRAPH #10



**BUILDING 21
SECTION A**

Subcontractor began installation of JumboTex WRB before Tyvek seams had been sealed with seam tape.

PHOTOGRAPH #11



**BUILDING 21
SECTION A**

At the direction of Delta, JumboTex WRB was removed and seam tape completed.

PHOTOGRAPH #12



**BUILDING 21
SECTION A**

Entrance doors recoated with primer prior to finish coat of paint.


PHOTOGRAPH #13



**BUILDING 21
UNIT #2125**

Window installation, Dupont flashing and interior sealant inspected for compliance to manufacturer's requirements and AAMA standard practice guidelines.

PHOTOGRAPH #14

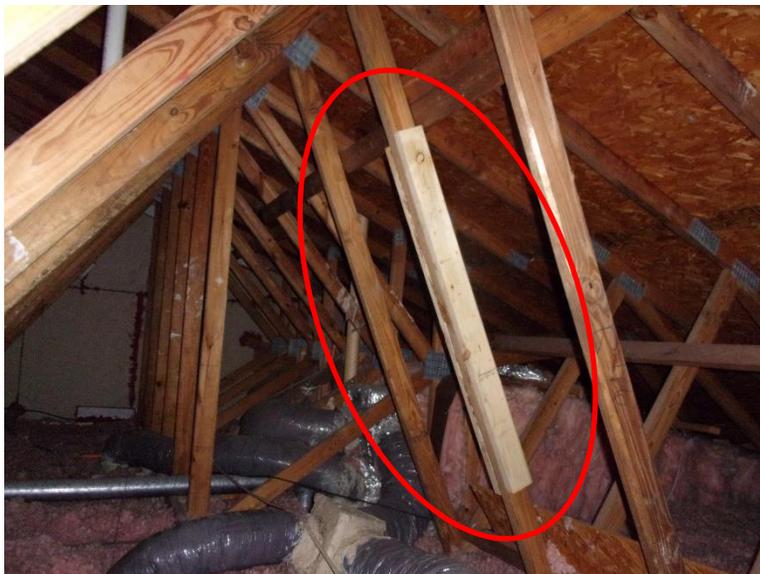

**BUILDING 21
UNIT #2125 - ATTIC**

Contractor has performed truss repairs and firewall repairs.

PHOTOGRAPH #15



**BUILDING 21
UNIT #2125 - ATTIC**

Contractor has performed truss repairs and firewall repairs.

PHOTOGRAPH #16



**BUILDING 21
UNIT #2123**

Window installation and Dupont flashing inspected for compliance to manufacturer's requirements and AAMA standard practice guidelines.

PHOTOGRAPH #17



**BUILDING 21
UNIT #2123 - ATTIC**

Contractor has performed truss repairs
and firewall repairs.

PHOTOGRAPH #18



**BUILDING 21
UNIT #2123 - ATTIC**

Contractor has performed truss repairs
and firewall repairs.

PHOTOGRAPH #19



**BUILDING 21
UNIT #2126**

Window installation and Dupont flashing inspected for compliance to manufacturer's requirements and AAMA standard practice guidelines.

PHOTOGRAPH #20



**BUILDING 21
UNIT #2126 - ATTIC**

Contractor has performed truss repairs and firewall repairs.

PHOTOGRAPH #21



**BUILDING 21
UNIT #2126 - ATTIC**

Contractor has performed truss repairs and firewall repairs.

PHOTOGRAPH #22



**BUILDING 21
UNIT #2124**

Gap at heads of triple set of new windows is too wide to meet manufacturer's NOA requirements for fastening of integral fin window.

PHOTOGRAPH #23



**BUILDING 21
UNIT #2124 - ATTIC**

Contractor has performed truss repairs
and firewall repairs.

PHOTOGRAPH #24



**BUILDING 21
UNIT #2124 - ATTIC**

Contractor has performed truss repairs
and firewall repairs.


PHOTOGRAPH #25



**BUILDING 20
SECTION H**

Contractor has begun framing repairs marked by Delta.

PHOTOGRAPH #26

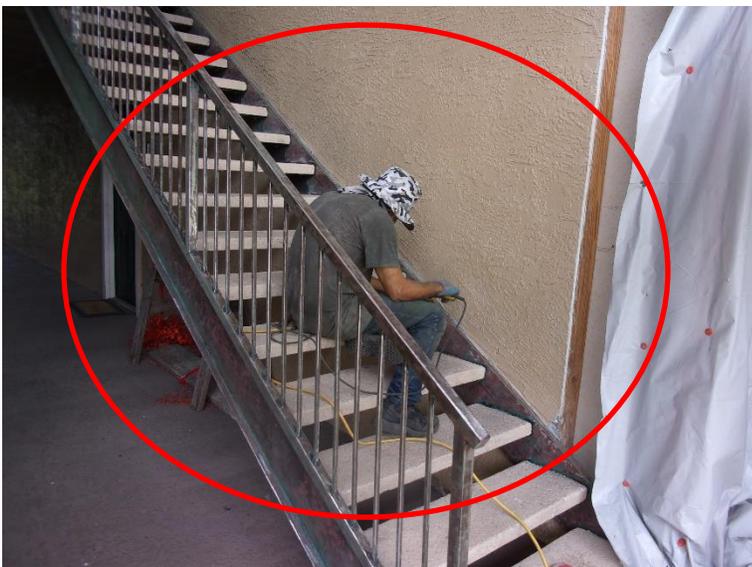

**BUILDING 20
SECTION A**

Preparation of stairway railings in breezeway for paint applications has begun.

PHOTOGRAPH #27



**BUILDING 20
SECTION B**

Framing and balcony deck damage observed and marked for repairs.

PHOTOGRAPH #28



**BUILDING 20
SECTION B**

Framing and balcony deck damage observed and marked for repairs.

PHOTOGRAPH #29



**BUILDING 20
SECTION B**

Framing and balcony deck damage observed and marked for repairs.

PHOTOGRAPH #30



**BUILDING 20
SECTION C**

Framing at breezeway, balconies and walls observed and marked for repairs.

PHOTOGRAPH #31



**BUILDING 20
SECTION C**

Framing at breezeway, balconies and walls observed and marked for repairs.

PHOTOGRAPH #32



**BUILDING 20
SECTION C**

Framing at breezeway, balconies and walls observed and marked for repairs.
