

PHOTOGRAPHS

PHOTOGRAPH #1



BUILDING 2 SECTION G

Stucco sub-contractor in process of applying metal lath and stucco accessories.

PHOTOGRAPH #2



BUILDING 2 SECTION F

Stucco sub-contractor in process of applying metal lath and stucco accessories.


PHOTOGRAPH #3



**BUILDING 2
SECTION F**

Super JumboTex 60 water resistant barrier overlapped as per manufacturers requirements.

PHOTOGRAPH #4

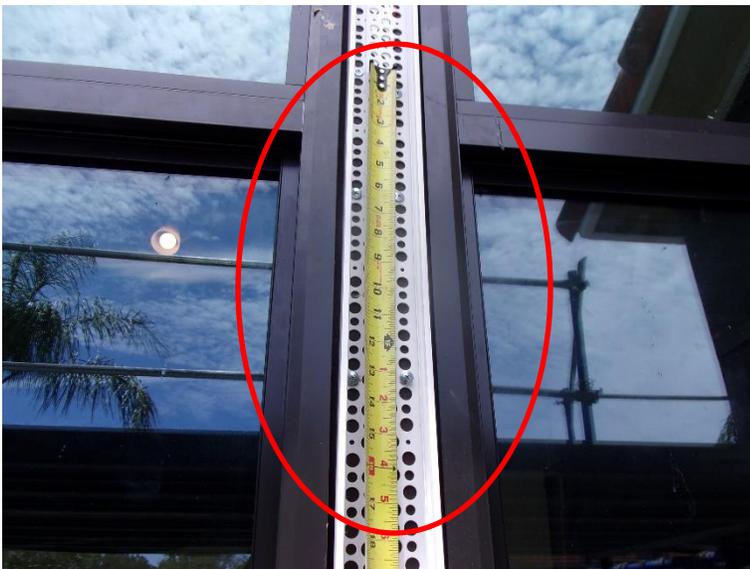

**BUILDING 2
SECTION F**

Vinyl stucco accessories attached at flange at no more than 7" intervals as per ASTM C1063.

PHOTOGRAPH #5



**BUILDING 2
SECTION E**

Contractor in process of priming breezeway handrails with Florida Paint Encapsulon industrial primer.

PHOTOGRAPH #6



**BUILDING 2
SECTION E**

Contractor in process of priming breezeway handrails with Florida Paint Encapsulon industrial primer.

PHOTOGRAPH #7



**BUILDING 2
SECTION E**

Front entrance doors have received finish coat of enamel paint.

PHOTOGRAPH #8



**BUILDING 2
SECTION D**

Contractor has begun plywood sheathing application at gable end wall.

PHOTOGRAPH #9



**BUILDING 2
SECTION D**

Owens Corning R-13 insulation provided were missing or damaged.

PHOTOGRAPH #10



**BUILDING 2
SECTION C**

Copper-Green wood preservative provided at lower two feet of wall framing.

PHOTOGRAPH #11



**BUILDING 2
SECTION C**

Simpson Strong-Tie straps provided at 16" O.C. at bearing wall.

PHOTOGRAPH #12



**BUILDING 2
SECTION C**

Contractor has applied primer at breezeway handrails with Florida Paint Encapsulon industrial primer.

PHOTOGRAPH #13



**BUILDING 2
SECTION B**

Selective balcony deck boards replaced as marked for repairs.

PHOTOGRAPH #14



**BUILDING 2
SECTION A**

Simpson Strong -Tie connector clips and screws provided at top plates and trusses.

PHOTOGRAPH #15



**BUILDING 2
SECTION A**

Built up concrete pedestal provided at
breezeway column.
