

## PHOTOGRAPHS

**PHOTOGRAPH #1**



### **BUILDING 6 SECTION A**

Contractor removed stucco on Section A and covered with plastic.

**PHOTOGRAPH #2**



### **BUILDING 6 SECTION B**

Contractor removed stucco on Section B and covered with plastic.

**PHOTOGRAPH #3**



**BUILDING 6  
SECTION C**

Contractor removed stucco on Section C and covered with plastic.

**PHOTOGRAPH #4**



**BUILDING 6  
SECTION D**

Contractor removed stucco on Section D and covered with plastic.

**PHOTOGRAPH #5**



**BUILDING 6  
SECTION A-D**

Contractor disposed stucco and debris from Sections A-D.

**PHOTOGRAPH #6**



**BUILDING 6  
SECTION G**

Stucco Sub-contractor installing Super JumboTex 60 Minute Weather-Resistive Barrier.

**PHOTOGRAPH #7**



**BUILDING 6  
SECTION G**

Stucco Sub-contractor installing Super JumboTex 60 Minute Weather-Resistive Barrier.

**PHOTOGRAPH #8**



**BUILDING 6  
SECTION H**

Stucco Sub-contractor installing Super JumboTex 60 Minute Weather-Resistive Barrier.

**PHOTOGRAPH #9**



**BUILDING 6  
SECTION H**

Stucco Sub-contractor provided over 2" horizontal overlap and 6" minimum vertical overlap.

**PHOTOGRAPH #10**



**BUILDING 3  
SECTION A**

Stucco Sub-contractor installed lath and accessories over Weather-Resistive Barrier.


**PHOTOGRAPH #11**



**BUILDING 3  
SECTION B**

Stucco Sub-contractor installed lath and accessories over Weather-Resistive Barrier.

**PHOTOGRAPH #12**

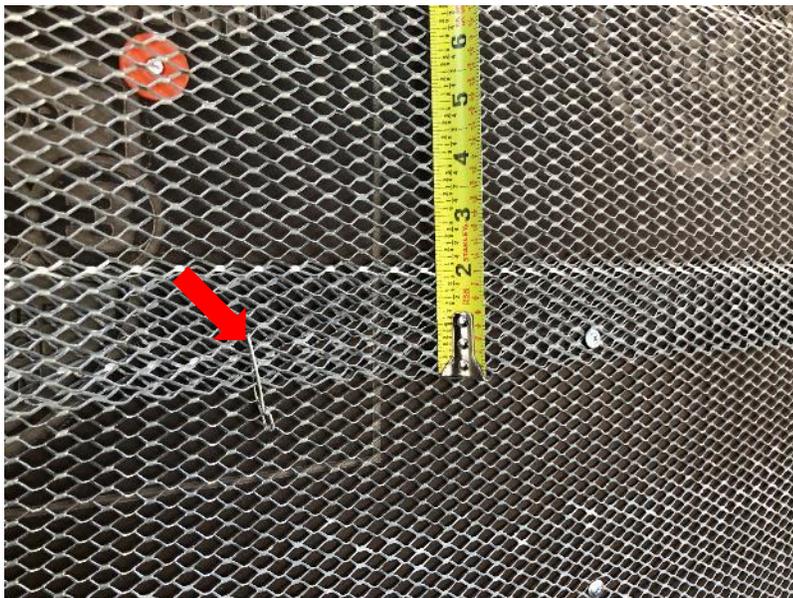

**BUILDING 3  
SECTION B**

Stucco Sub-contractor overlapped lath 2" minimum per the construction drawings and installed tie wire between fasteners.

**PHOTOGRAPH #13**



**BUILDING 3  
SECTION C**

Stucco Sub-contractor installed lath and accessories over Weather-Resistive Barrier.

**PHOTOGRAPH #14**



**BUILDING 3  
SECTION C**

Kickout flashing and accessories have been installed per the contract drawings.

**PHOTOGRAPH #15**



**BUILDING 3  
SECTION D**

Stucco Sub-contractor installed lath and accessories over Weather-Resistive Barrier.


**PHOTOGRAPH #16**



**BUILDING 3  
SECTION D**

Stucco Sub-contractor installed lath and accessories over Section D area that required truss repairs.


**PHOTOGRAPH #17**

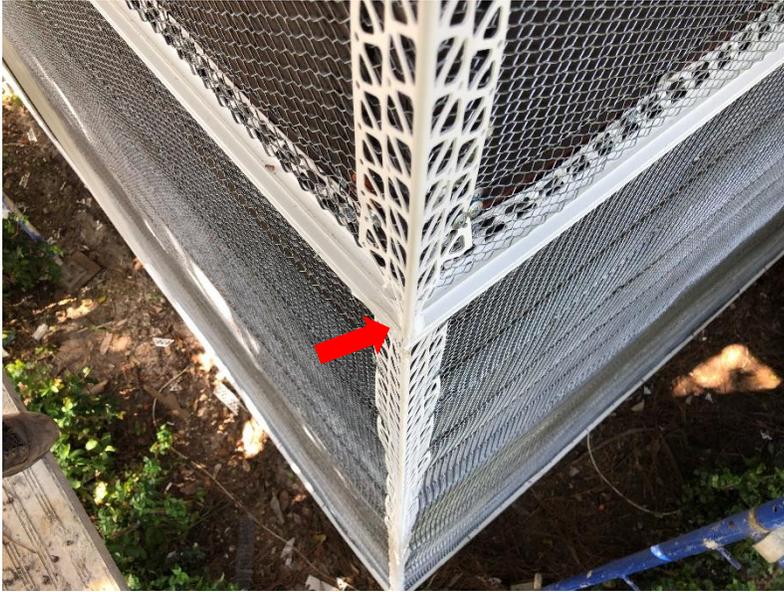

**BUILDING 3  
SECTION D**

MasterSeal NP 150 sealant was applied to accessory ends, corners, and intersections.

**PHOTOGRAPH #18**

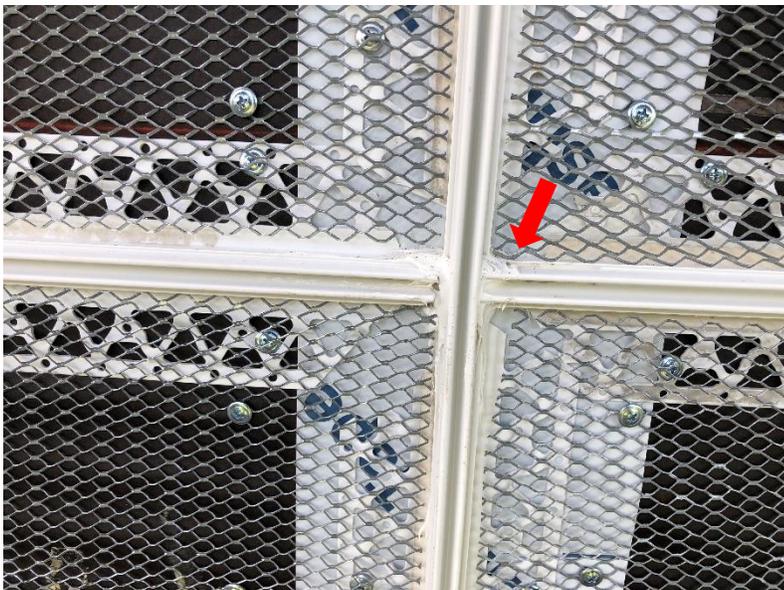

**BUILDING 3  
SECTION D**

MasterSeal NP 150 sealant was applied to accessory ends, corners, and intersections.

**PHOTOGRAPH #19**



**BUILDING 3  
SECTION D**

MasterSeal NP 150 sealant was applied to accessory ends, corners, and intersections.

**PHOTOGRAPH #20**



**BUILDING 3  
SECTION E**

Stucco Sub-contractor applied scratch coat and brown coat.

**PHOTOGRAPH #21**



**BUILDING 3  
SECTION F**

Stucco Sub-contractor applied stucco final coat.

**PHOTOGRAPH #22**



**BUILDING 3  
SECTION F**

Contractor cleaned construction debris and trash from landscaped areas.

**PHOTOGRAPH #23**



**BUILDING 3  
SECTION G**

Stucco Sub-contractor applied stucco final coat.

**PHOTOGRAPH #24**



**BUILDING 3  
SECTION H**

Stucco Sub-contractor applied final coat.

**PHOTOGRAPH #25**



**BUILDING 3  
SECTION H**

Stucco Sub-contractor applied MasterSeal NP 150 sealant around windows and inside stucco corners.

**PHOTOGRAPH #26**



**BUILDING 3  
SECTION H**

Stucco Sub-contractor applied MasterSeal NP 150 sealant around windows and inside stucco corners.

**PHOTOGRAPH #27**



**BUILDING 3  
SECTION H**

Stucco Sub-contractor applied MasterSeal NP 150 sealant around windows and inside stucco corners.

**PHOTOGRAPH #28**



**BUILDING 3  
SECTIONS E-H**

Stucco Sub-contractor used approved Cemex Broco Stucco Cement to mix stucco on-site.

**PHOTOGRAPH #29**



**BUILDING 3  
SECTIONS E-H**

Stucco Sub-contractor used approved Cemex Broco Stucco Cement to mix stucco on-site.
