

## PHOTOGRAPHS


PHOTOGRAPH #1



### BUILDING 6 SECTION H

Jumbo Tex super 60 WRB applied and stucco accessories in progress.

PHOTOGRAPH #2

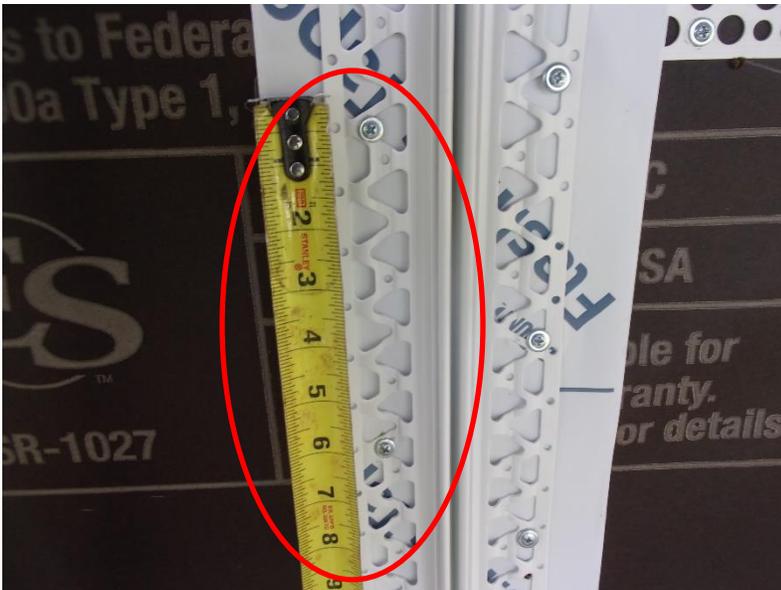

### BUILDING 6 SECTION F

Vinyl stucco joints attached over Dupont flashing at 7" intervals as per specifications.

**PHOTOGRAPH #3**



**BUILDING 6  
SECTION F**

New soffit and soffit vent installed and prepared for prime and painting.

**PHOTOGRAPH #4**



**BUILDING 6  
SECTION E**

Contractor has approved erecting of access scaffold as per safety program process.

**PHOTOGRAPH #5**



**BUILDING 6  
SECTION D**

Framing repairs have begun at wall studs and window openings with 2"X4" southern yellow pine.

**PHOTOGRAPH #6**



**BUILDING 6  
SECTION D**

Window opening repairs performed at jams, sills, and jacks.

**PHOTOGRAPH #7**



**BUILDING 6  
SECTION D**

3 1/2" 16P framing nails used for framing repairs as per drawings.

**PHOTOGRAPH #8**



**BUILDING 6  
SECTION D**

Gable end structural support framing in progress as per drawings.

**PHOTOGRAPH #9**



**BUILDING 6  
SECTION D**

Drywall damage identified at **Unit #628** will require removal and replacement.

**PHOTOGRAPH #10**



**BUILDING 6  
STORAGE AREA**

Sheathing plywood and wood framing materials delivered.

**PHOTOGRAPH #11**



**BUILDING 3  
SECTION B**

Newly painted balcony railings placed upon balconies for installation.

**PHOTOGRAPH #12**



**BUILDING 3  
STORAGE AREA**

Storage and laydown area at parking lot has been cleared out and re-opened for tenants parking.

**PHOTOGRAPH #13**



**BUILDING 3  
STORAGE AREA**

Florida Paints Encapsulon Epoxy Mastic Primer applied to balcony railings.

**PHOTOGRAPH #14**



**BUILDING 3  
STORAGE AREA**

Florida Paints Encapsulon Epoxy Mastic Primer applied to balcony railings.

**PHOTOGRAPH #15**



**BUILDING 3  
STORAGE AREA**

Florida Paints Sundeavor high  
performance urethan enamel, spray  
applied to balcony railings.
