

PHOTOGRAPH #1



**BUILDING 12
SECTION A**

Subcontractor has applied scratch coat of three coat 7/8" stucco finish system as per specifications.

PHOTOGRAPH #2



**BUILDING 12
SECTION A**

Subcontractor applying brown and finish coats of three coat 7/8" stucco finish system as per specifications.

PHOTOGRAPH #3



**BUILDING 12
SECTION A**

Stucco Sub-Contractor mixing Broco bag stucco cement mix with sand and water.

PHOTOGRAPH #4



**BUILDING 12
SECTION A- UNIT 1211**

Contractor performing dry wall and finish repairs at interior units around new PGT window openings.


PHOTOGRAPH #5



**BUILDING 12
SECTION A- UNIT 1211**

New urethane sealant applied at window frame to Dupont flashing at windowsill as per manufacturer's installation instructions and drawings.

PHOTOGRAPH #6

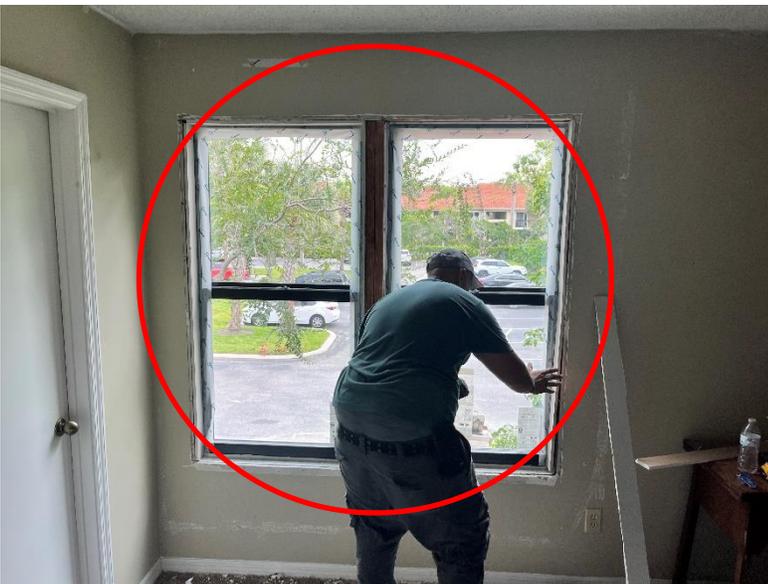

**BUILDING 12
SECTION A- UNIT 1221**

Contractor performing dry wall and finish repairs at interior units around new PGT window openings.

PHOTOGRAPH #7



**BUILDING 12
SECTION B**

Subcontractor has applied scratch coat of three coat 7/8" stucco finish system as per specifications.

PHOTOGRAPH #8



**BUILDING 12
SECTION B UNIT 1213**

Contractor performing dry wall and finish repairs at interior units around new PGT window openings.

PHOTOGRAPH #9



**BUILDING 12
SECTION B UNIT 1223**

Contractor has completed dry wall and finish repairs at interior units around new PGT window openings

PHOTOGRAPH #10



**BUILDING 12
SECTION C**

Subcontractor has applied finish texture coat of three coat 7/8" stucco finish system as per specifications.

PHOTOGRAPH #11



**BUILDING 12
SECTION D**

Subcontractor has applied finish texture coat of three coat 7/8" stucco finish system as per specifications.

PHOTOGRAPH #12



**BUILDING 12
SECTION F- UNIT 1214**

Delta checking window gap at interior jambs for compliance with PGT product approval requirements and drawings.

PHOTOGRAPH #13



**BUILDING 12
SECTION F- UNIT 1214**

Delta checking window gap at interior head for compliance with PGT product approval requirements and drawings.

PHOTOGRAPH #14



**BUILDING 9
SECTION H**

Contractor has installed new plywood soffit at gable end wall.

PHOTOGRAPH #15



**BUILDING 9
SECTION H**

DuPont flashing installed at head of window extends out beyond outer edges of Jamb flashing as per drawings.

PHOTOGRAPH #16



**BUILDING 9
SECTION G**

New PGT SH7700A single hung windows installed with Dupont Flashings as per drawing and specifications.

PHOTOGRAPH #17



**BUILDING 9
SECTION G**

New plywood soffit and vinyl vent installed as per drawings.

PHOTOGRAPH #18



**BUILDING 9
SECTION F**

New PGT SH7700A single hung windows installed with Dupont Flashings as per drawing and specifications.


PHOTOGRAPH #19



**BUILDING 9
SECTION F**

New plywood soffit and vinyl vent installation in progress.

PHOTOGRAPH #20

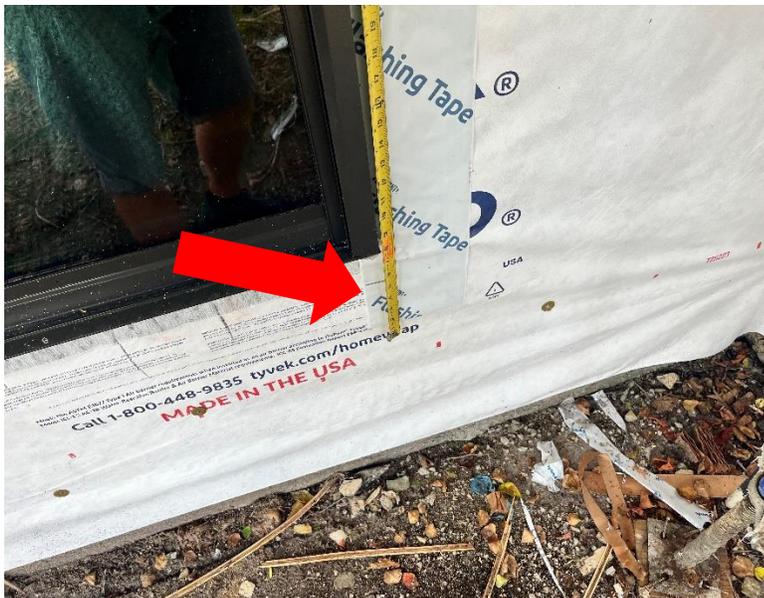

**BUILDING 9
SECTION E**

Dupont Flashing Tape applied over window flange onto Tyvek HomeWrap extends down past window frame as per drawings and manufacturer's recommendations.

PHOTOGRAPH #21



**BUILDING 9
SECTION D**

Contractor has removed stucco and previous sheathing for inspection and marking of damaged framing by Delta.

PHOTOGRAPH #22



**BUILDING 9
SECTION D**

Single window header damaged and marked for removal and replacement.

PHOTOGRAPH #23



**BUILDING 9
SECTION D**

Damaged 2nd floor top plate and gable end truss marked for repairs.

PHOTOGRAPH #24



**BUILDING 9
SECTION C**

Previous roof leaks have damaged roof sheathing above the soffit.

PHOTOGRAPH #25



**BUILDING 9
SECTION B**

Triple window headers and top plate damaged and marked for repairs.

PHOTOGRAPH #26



**BUILDING 9
SECTION B – UNIT #923**

Damaged balcony built up rail beam and deck boards marked for full repairs.

PHOTOGRAPH #27



**BUILDING 9
SECTION B-UNIT 923**

Contractor has removed deck boards and built-up beam, exposing additional damage at framing below doorway.

PHOTOGRAPH #28



**BUILDING 9
SECTION B - UNIT 925**

Contractor has removed deck boards and built-up beam, exposing additional damage at framing below doorway.

PHOTOGRAPH #29



**BUILDING 9
SECTION B – UNIT 925**

Original cedar beam, door header and all framing damaged will require removal and new framing members.
